



RCP, Inc

801 Louisiana, Ste.200  
Houston, Texas 77002

Redacted

August 4, 2011

Pacific Gas and Electric Company  
350 N. Wiget  
Walnut Creek, CA 94598  
Attention: Redacted

Test Contractor: Milbar Hydro-test Incorporated -- FY12-112  
Asset Owner: Pacific Gas and Electric Company -- 41497309  
Construction Contractor: Snelson -- 41474005-T74  
Test Section: PG&E T-74 Line 300A, MP 499.77 - 502.23  
Test Date: August 4, 2011  
Certificate Number: RCP 61362 - T-74, L-300A

To whom it may concern,

This letter is to certify that the hydrostatic test performed on pipe owned by Pacific Gas and Electric Company and tested by Milbar Hydro-test Incorporated met the requirements of the Code of Federal Regulations, Title 49, Part 192, Subpart J (Class 3).

The test segment was subjected to a spike pressure test of 1090 psig for 30 minutes, without observed leakage or yielding of the pipe segment. The 30 minute spike test and subsequent pressure reduction with volume bleed was included and is part of the 8.72 hour test duration period.

This hydrostatic test was completed successfully. Pressure was maintained on the test facilities in excess of 8.72 continuous hours without evidence of a leak failure. Water was the test medium. At the highest elevation point in the test section, the calculated test pressure was 1023 psig and the established MAOP is 682 psig.

Pressure decreased 67 psi during the test. 22,272.00 ounces of fluid was intentionally released from the test section. Net corrected volumetric change from beginning of the test to the end of the test is calculated to be 7,082.09 ounces, loss, which is equivalent to a 0.66 °F change in pipe temperature and within the error attributed to the temperature measurement instrumentation utilized.

Test pressure did not remain steady even though no leaks were observed. The volumetric loss is attributed to the error characteristic of the temperature measurement instrumentation utilized.

Sincerely,

Redacted

cc. file

C:\Users\Redac\Documents\PG&E Pressure tests\T-74\

RCP 61362 - T-74, L-300A, MP 499.77 - 502.23

Letter

Page 1 of 11

8/4/2011

SB\_GT&S\_0047012



## Hydrostatic Test Certification

Company	Pacific Gas and Electric Company	Job Number	41497309
Construction Co.	Snelson	Job Number	41474005-T74
Hydro. Test Co.	Milbar Hydro-test Incorporated	Project No.	FY12-112
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23		
File Name	RCP 61362 - T-74, L-300A		

### Hydrostatic Test Pressure

APPLICABLE CODE FOR CERTIFICATION:	Test Date:	4-Aug-11
<b>Code of Federal Regulations, Title 49, Part 192, Subpart J (Class 3)</b>		

This is to certify that the pipeline or pipeline section(s) described below was hydrostatically pressure tested in accordance with the following procedure:

Pipeline:	PG&E T-74 Line 300A, MP 499.77 - 502.23	From:	0+00	To:	184+08
-----------	---	-------	------	-----	--------

### Pipe Data

Segment	Length	Diameter	Wall Thickness	Specification	100% SMYS
1	60 ft	34.000 in.	0.505 in.	API5L-X60, DSAW, Arc Weld, Steel	1,782 psi
2	1,867 ft	36.000 in.	0.500 in.	API5L-X60, DSAW, Arc Weld, Steel	1,667 psi
3	918 ft	36.000 in.	0.432 in.	API5L-X60, DSAW, Arc Weld, Steel	1,440 psi
4	2,000 ft	36.000 in.	0.414 in.	API5L-X65, DSAW, Arc Weld, Steel	1,495 psi
5	7 ft	34.000 in.	0.562 in.	API5L-X60, DSAW, Arc Weld, Steel	1,984 psi
6	362 ft	34.000 in.	0.505 in.	API5L-X60, DSAW, Arc Weld, Steel	1,782 psi
7	6,876 ft	34.000 in.	0.500 in.	API5L-X46, DSAW, Arc Weld, Steel	1,353 psi
8	1,532 ft	34.000 in.	0.383 in.	API5L-X60, DSAW, Arc Weld, Steel	1,352 psi
9	40 ft	34.000 in.	0.500 in.	API5L-X65, DSAW, Arc Weld, Steel	1,912 psi
10	22 ft	30.000 in.	0.375 in.	API5L-X60, DSAW, Arc Weld, Steel	1,500 psi
12	49 ft	6.625 in.	0.280 in.	API5L-Grade B, SM, Arc Weld, Steel	2,958 psi

### Initial Test Conditions

Pressure at Test Point:	1,090 psig	Date/Time:	8/4/11 3:02 AM	Pipe Temperature	
				Unrestrained:	73.0 °F
Ambient Temperature:	66.0 °F	Elevation @ Test Point:	55.0 ft	Restrained:	75.0 °F
Pressure @ High Point (Cal/Measure):	1,090 psig	Elevation @ High Point:	55.0 ft	Location:	0+00
Pressure @ Low Point (Cal/Measure):	1,105 psig	Elevation @ Low Point:	20.0 ft	Location:	135+00

### Final Test Conditions

Pressure at Test Point:	1,023 psig	Date/Time:	8/4/11 11:45 AM	Pipe Temperature	
				Unrestrained:	78.0 °F
Ambient Temperature:	72.0 °F	Elevation @ Test Point:	65.0 ft	Restrained:	75.0 °F
Pressure @ High Point (Cal/Measure):	1,023 psig	Elevation @ High Point:	55.0 ft	Location:	0+00
Pressure @ Low Point (Cal/Measure):	1,038 psig	Elevation @ Low Point:	20.0 ft	Location:	135+00
Total Fluid Injected:				Volume loss	
Total Fluid Withdrawn:	22272.00 fluid ounces				
Net Change in Volume of the Test Section ± (+ Gain, - Loss):	(7,082.09) oz	loss	(0.0087)%	(0.665) °F equivalent	

Test Duration: 8.72 hours

Minimum Test Pressure:	Test Point	1,023 psig	Max Elevation	1,023 psig	Min Elevation	1,038 psig
Maximum Test Pressure:		1,090 psig		1,090 psig		1,105 psig
% SMYS :		80.6%		80.6%		81.8%

Minimum Test Pressure (Calculated/Measured): 1,023 psig

Maximum Allowable Operating Pressure:	DOT Part 192	Test Factor= 1.50	682 psig
---------------------------------------	--------------	-------------------	----------

Were leaks observed?	No	Explain:
Acceptable Hydrostatic Test?	Yes	<p>The test segment was subjected to a spike pressure test of 1090 psig for 30 minutes, without observed leakage or yielding of the pipe segment. The 30 minute spike test and subsequent pressure reduction with volume bleed was included and is part of the 8.72 hour test duration period.</p> <p>No leaks were observed during the test period. The test section included 13,562 feet of buried and 171 feet of exposed pipe. Pressure lost 67 psi during the test. The buried pipe segment fluid temperature remained steady and the exposed pipe segment gained 5°F.</p> <p>22,272.00 ounces of fluid was intentionally released from the test section. Net corrected volumetric change from beginning of the test to the end of the test is calculated to be 7,082.09 ounces, loss, which is equivalent to a 0.66 °F change in pipe temperature and within the error attributed to the temperature measurement instrumentation utilized.</p> <p>Test pressure did not remain steady even though no leaks were observed. The volumetric loss is attributed to the error characteristic of the temperature measurement instrumentation utilized.</p>
Remarks	Additional pipe included in this test segment. 9-3.5", .216 wall, GrB, SMLS, 9- 3.5", .141 wall, GrA, 25,000 SMYS	

Redacted

4-Aug-11



# Dead Weight Log Sheet

Owner Company	Pacific Gas and Electric Company	Job Number	41497309
Construction Co.	Snelson	Job Number	41474005-T74
Testing Co.	Milbar Hydro-test Incorporated	Project No.	FY12-112
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23		
File Name	RCP 61362 - T-74, L-300A		

Date

4-Aug-11

## Test Log

Log No.	Test Period		Test Pressure	Temperature °F			Remarks		
	Date	Time		Ambient	Pipe				
					Unrestrained	Restrained	Comment	Bleed	Inject
1	8/4/11	2:29 AM	760 psig	66 °F	73 °F	75 °F	Start Spike		
2	8/4/11	2:30 AM	770 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
3	8/4/11	2:31 AM	780 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
4	8/4/11	2:32 AM	790 psig	66 °F	73 °F	75 °F	Inject		4,371 oz.
5	8/4/11	2:33 AM	800 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
6	8/4/11	2:34 AM	810 psig	66 °F	73 °F	75 °F	Inject		4,724 oz.
7	8/4/11	2:35 AM	820 psig	66 °F	73 °F	75 °F	Inject		4,230 oz.
8	8/4/11	2:36 AM	830 psig	66 °F	73 °F	75 °F	Inject		4,653 oz.
9	8/4/11	2:37 AM	840 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
10	8/4/11	2:38 AM	850 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
11	8/4/11	2:39 AM	860 psig	66 °F	73 °F	75 °F	Inject		4,653 oz.
12	8/4/11	2:40 AM	870 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
13	8/4/11	2:41 AM	880 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
14	8/4/11	2:42 AM	890 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
15	8/4/11	2:43 AM	900 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
16	8/4/11	2:44 AM	910 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
17	8/4/11	2:45 AM	920 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
18	8/4/11	2:46 AM	930 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
19	8/4/11	2:47 AM	940 psig	66 °F	73 °F	75 °F	Inject		4,301 oz.
20	8/4/11	2:48 AM	950 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
21	8/4/11	2:49 AM	960 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
22	8/4/11	2:50 AM	970 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
23	8/4/11	2:51 AM	980 psig	66 °F	73 °F	75 °F	Inject		4,301 oz.
24	8/4/11	2:52 AM	990 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
25	8/4/11	2:53 AM	1,000 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
26	8/4/11	2:54 AM	1,010 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
27	8/4/11	2:55 AM	1,020 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
28	8/4/11	2:56 AM	1,030 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
29	8/4/11	2:57 AM	1,040 psig	66 °F	73 °F	75 °F	Inject		4,512 oz.
30	8/4/11	2:58 AM	1,050 psig	66 °F	73 °F	75 °F	Inject		4,653 oz.
31	8/4/11	2:59 AM	1,060 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
32	8/4/11	3:00 AM	1,070 psig	66 °F	73 °F	75 °F	Inject		4,442 oz.
33	8/4/11	3:01 AM	1,080 psig	66 °F	73 °F	75 °F	Inject		4,583 oz.
34	8/4/11	3:01 AM	1,090 psig	66 °F	73 °F	75 °F	Inject		4,653 oz.
35	8/4/11	3:02 AM	1,090 psig	66 °F	73 °F	75 °F	On Test		
36	8/4/11	3:12 AM	1,089 psig	66 °F	74 °F	75 °F			
37	8/4/11	3:22 AM	1,089 psig	66 °F	73 °F	75 °F			
38	8/4/11	3:32 AM	1,089 psig	66 °F	73 °F	75 °F	End Spike		
39	8/4/11	3:42 AM	1,079 psig	66 °F	73 °F	75 °F	Bleed	3,840 oz.	
40	8/4/11	3:52 AM	1,069 psig	66 °F	73 °F	75 °F	Bleed	3,840 oz.	
41	8/4/11	4:02 AM	1,059 psig	66 °F	73 °F	75 °F	Bleed	3,840 oz.	
42	8/4/11	4:15 AM	1,031 psig	65 °F	73 °F	75 °F	Bleed	10,752 oz.	
43	8/4/11	4:30 AM	1,030 psig	65 °F	73 °F	75 °F	Cool		



# Dead Weight Log Sheet

Owner Company	Pacific Gas and Electric Company						Job Number	41497309					
Construction Co.	Snelson						Job Number	41474005-T74					
Testing Co.	Milbar Hydro-test Incorporated						Project No.	FY12-112					
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23												
File Name	RCP 61362 - T-74, L-300A												
Date 4-Aug-11			Test Log										
Log No.	Test Period		Test Pressure	Temperature °F			Remarks						
	Date	Time		Ambient	Unrestrained	Restrained							
44	8/4/11 4:45 AM	1,030 psig	65 °F	73 °F	75 °F								
45	8/4/11 5:00 AM	1,030 psig	65 °F	73 °F	75 °F								
46	8/4/11 5:15 AM	1,029 psig	65 °F	73 °F	75 °F								
47	8/4/11 5:30 AM	1,029 psig	65 °F	73 °F	75 °F								
48	8/4/11 5:45 AM	1,029 psig	65 °F	73 °F	75 °F								
49	8/4/11 6:00 AM	1,029 psig	65 °F	73 °F	75 °F								
50	8/4/11 6:15 AM	1,028 psig	65 °F	73 °F	75 °F	Cloud Cover							
51	8/4/11 6:30 AM	1,028 psig	65 °F	73 °F	75 °F								
52	8/4/11 6:45 AM	1,027 psig	65 °F	73 °F	75 °F								
53	8/4/11 7:00 AM	1,027 psig	65 °F	73 °F	75 °F								
54	8/4/11 7:15 AM	1,027 psig	65 °F	73 °F	75 °F								
55	8/4/11 7:30 AM	1,027 psig	66 °F	73 °F	75 °F								
56	8/4/11 7:45 AM	1,026 psig	65 °F	73 °F	75 °F								
57	8/4/11 8:00 AM	1,026 psig	66 °F	73 °F	75 °F								
58	8/4/11 8:15 AM	1,026 psig	67 °F	73 °F	75 °F								
59	8/4/11 8:30 AM	1,025 psig	66 °F	73 °F	75 °F								
60	8/4/11 8:45 AM	1,025 psig	68 °F	73 °F	75 °F								
61	8/4/11 9:00 AM	1,025 psig	66 °F	74 °F	75 °F								
62	8/4/11 9:15 AM	1,025 psig	66 °F	75 °F	75 °F								
63	8/4/11 9:30 AM	1,024 psig	69 °F	75 °F	75 °F								
64	8/4/11 9:45 AM	1,024 psig	71 °F	75 °F	75 °F								
65	8/4/11 10:00 AM	1,024 psig	69 °F	75 °F	75 °F								
66	8/4/11 10:15 AM	1,024 psig	69 °F	76 °F	75 °F	Partly Cloudy							
67	8/4/11 10:30 AM	1,024 psig	68 °F	76 °F	75 °F								
68	8/4/11 10:45 AM	1,024 psig	70 °F	77 °F	75 °F								
69	8/4/11 11:00 AM	1,023 psig	70 °F	77 °F	75 °F								
70	8/4/11 11:15 AM	1,023 psig	71 °F	77 °F	75 °F								
71	8/4/11 11:30 AM	1,023 psig	71 °F	78 °F	75 °F								
72	8/4/11 11:45 AM	1,023 psig	72 °F	78 °F	75 °F	End of Test							
							Spike Test	148,618.7 oz.					
							Hydrostatic Test	22,272.0 oz.					
Were leaks observed during the test period?			Exposed and buried pipe, no leaks observed.			<table border="1"> <tr> <td>High Test Pressure:</td><td>1,090 psig</td> </tr> <tr> <td>Low Test Pressure:</td><td>1,023 psig</td> </tr> </table>				High Test Pressure:	1,090 psig	Low Test Pressure:	1,023 psig
High Test Pressure:	1,090 psig												
Low Test Pressure:	1,023 psig												



## Pipe Segment Volume Calculations

Company	Pacific Gas and Electric Company							Job Number	41497309		
Construction Co.	Snelson							Job Number	41474005-T74		
Hydro. Test Co.	Milbar Hydro-test Incorporated							Project No.	FY12-112		
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23							WATER			
File Name	RCP 61362 - T-74, L-300A										
General Pipe Data											
Description	Segment										
	1	2	3	4	5	6	7	8	9	10	12
Restrained or Unrestrained?	Unrestrained	Restrained	Restrained	Restrained	Restrained	Restrained	Restrained	Unrestrained	Unrestrained	Unrestrained	Unrestrained
Outside Diameter	34.000 in.	38.000 in.	36.000 in.	36.000 in.	34.000 in.	34.000 in.	34.000 in.	34.000 in.	34.000 in.	30.000 in.	6.625 in.
Wall Thickness	0.505 in.	0.500 in.	0.432 in.	0.414 in.	0.562 in.	0.505 in.	0.500 in.	0.383 in.	0.500 in.	0.375 in.	0.280 in.
Inside Diameter	32.990 in.	35.000 in.	35.138 in.	35.172 in.	32.876 in.	32.990 in.	33.000 in.	33.234 in.	33.000 in.	29.250 in.	6.065 in.
Spec./Grade	API5L-X60	API5L-X60	API5L-X60	API5L-X65	API5L-X60	API5L-X60	API5L-X46	API5L-X60	API5L-X65	API5L-X60	API5L-Grade B
Length Unrestrained	60 ft										40 ft
Length Restrained	1,867 ft										22 ft
Temperature ~ On Test	73 °F	75 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	73.0 °F	73.0 °F	73.0 °F
Temperature ~ End of Test	78 °F	75 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	75.0 °F	78.0 °F	78.0 °F	78.0 °F
Pressure ~ On Test	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig	1,090 psig
Pressure ~ End of Test	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig	1,023 psig
Unrestrained Pipe											
Sum:	Vo	5,282.98 gal		Vip1	5,310.41 gal		Vip2	5,305.12 gal			
		676,222 oz.			679,733 oz.				679,055 oz.		
Vo Unrestrained	2,664 gal							1,777 gal	768 gal	73.5 gal	
Fwp 1	1.003341							1.003341	1.003341	1.003341	
Fpp 1	1.002967							1.002998	1.003543	1.000984	
Fpt 1	1.000237							1.000237	1.000237	1.000237	
Fwt 1	1.001423							1.001423	1.001423	1.001423	
Fpwt 1 = Fpt/Fwt	0.998815							0.998815	0.998815	0.998815	
Vip 1 = Vo(Fwp)(Fpp)(Fpwt)	2,677.91 gal							1,786.41 gal	772.33 gal	73.77 gal	
Fwp 2	1.003135							1.003135	1.003135	1.003135	
Fpp 2	1.002785							1.002813	1.003325	1.000923	
Fpt 2	1.000328							1.000328	1.000328	1.000328	
Fwt 2	1.002122							1.002122	1.002122	1.002122	
Fpwt 2 = Fpt/Fwt	0.998209							0.998209	0.998209	0.998209	
Vip 2 = Vo(Fwp)(Fpp)(Fpwt)	2,676.25 gal							1,784.63 gal	771.54 gal	73.71 gal	
Restrained Pipe											
Sum:	Vo	631,424.28 gal		Vip1	634,141.78 gal		Vip2	633,917.75 gal			
		80,822,308 oz.			81,170,147 oz.			81,141,472 oz.			
Vo Unrestrained		93,312 gal	46,239 gal	100,945 gal	309 gal	16,074 gal	305,508 gal	69,037 gal			
Fwp 1		1.003341	1.003341	1.003341	1.003341	1.003341	1.003341	1.003341			
Fpp 1		1.002368	1.002743	1.002663	1.001968	1.002214	1.002236	1.002923			
Fpt 1		1.000182	1.000182	1.000182	1.000182	1.000182	1.000182	1.000182			
Fwt 1		1.001688	1.001688	1.001688	1.001688	1.001688	1.001688	1.001688			
Fpwt 1 = Fpt/Fwt		0.998496	0.998496	0.998496	0.998496	0.998496	0.998496	0.998496			
Vip 1 = Vo(Fwp)(Fpp)(Fpwt)		93,705 gal	46,451 gal	101,419 gal	310 gal	16,139 gal	306,752 gal	69,366 gal			
Fwp 2		1.003135	1.003135	1.003135	1.003135	1.003135	1.003135	1.003135			
Fpp 2		1.002226	1.002578	1.002690	1.001869	1.002081	1.002102	1.002747			
Fpt 2		1.000182	1.000182	1.000182	1.000182	1.000182	1.000182	1.000182			
Fwt 2		1.001688	1.001688	1.001688	1.001688	1.001688	1.001688	1.001688			
Fpwt 2 = Fpt/Fwt		0.998496	0.998496	0.998496	0.998496	0.998496	0.998496	0.998496			
Vip 2 = Vo(Fwp)(Fpp)(Fpwt)		93,672 gal	46,433 gal	101,381 gal	310 gal	16,134 gal	306,648 gal	69,339 gal			
Combined Pipe											
Sum:	Vo	636,707.27 gal		Vip1	639,452.19 gal		Vip2	639,222.86 gal			
		81,498,530 oz.			81,849,881 oz.			81,820,526 oz.			



## Pipe Segment Volume Allowance Calculations

Company	Pacific Gas and Electric Company						Job Number	41497309			
Construction Co.	Snelson						Job Number	41474005-T74			
Hydro. Test Co.	Milbar Hydro-test Incorporated						Project No.	FY12-112			
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23							WATER			
File Name	RCP 61362 - T-74, L-300A										
General Pipe Data											
Description	Segment										
	1	2	3	4	5	6	7	8	9	10	12
Restrained or Unrestrained?	Unrestrained	Restrained	Restrained	Restrained	Restrained	Restrained	Restrained	Unrestrained	Unrestrained	Unrestrained	
Outside Diameter	34.000 in.	36.000 in.	36.000 in.	36.000 in.	34.000 in.	34.000 in.	34.000 in.	34.000 in.	30.000 in.	6.625 in.	
Wall Thickness	0.505 in.	0.500 in.	0.432 in.	0.414 in.	0.562 in.	0.505 in.	0.500 in.	0.383 in.	0.500 in.	0.280 in.	
Inside Diameter	32.990 in.	35.000 in.	35.136 in.	35.172 in.	32.876 in.	32.990 in.	33.000 in.	33.234 in.	33.000 in.	6.065 in.	
Spec./Grade	API5L-X60	API5L-X60	API5L-X60	API5L-X65	API5L-X60	API5L-X60	API5L-X46	API5L-X60	API5L-X65	API5L-X60	
Length Unstrained	60.00 ft								40 ft	22 ft	
Length Restrained		1,867 ft	918 ft	2,000 ft	7 ft	362 ft	6,876 ft	1,532 ft			
Temperature - On Test	75 °F	74 °F	74 °F	74 °F	74 °F	74 °F	74 °F	75 °F	75 °F	75 °F	
Temperature - End of Test	76 °F	75 °F	75 °F	75 °F	75 °F	75 °F	75 °F	76 °F	76 °F	76 °F	
Pressure - On Test	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	
Pressure - End of Test	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	1,056 psig	
Unrestrained Pipe											
Sum:	Vo	5,282.98 gal		Vlp1	5,308.15 gal		Vlp2	5,307.58 gal			
		676,222 oz.			679,443 oz.			679,371 oz.			
Vo Unrestrained	2,664 gal							1,777 gal	768 gal	74 gal	
Fwp 1	1.003237							1.003237	1.003237	1.003237	
Fpp 1	1.002874							1.002904	1.003432	1.000953	
Fpt 1	1.000273							1.000273	1.000273	1.000273	
Fwt 1	1.001688							1.001688	1.001688	1.001688	
Fpwt 1 = Fpt/Fwt	0.998587							0.998587	0.998587	0.998587	
Vlp 1 = Vo(Fwp)(Fpp)(Fpwt)	2,676.77 gal							1,786 gal	772 gal	74 gal	
Fwp 2	1.003237							1.003237	1.003237	1.003237	
Fpp 2	1.002874							1.002904	1.003432	1.000953	
Fpt 2	1.000291							1.000291	1.000291	1.000291	
Fwt 2	1.001813							1.001813	1.001813	1.001813	
Fpwt 2 = Fpt/Fwt	0.998481							0.998481	0.998481	0.998481	
Vlp = Vo(Fwp)(Fpp)(Fpwt)	2,676.48 gal							1,785 gal	772 gal	74 gal	
Restrained Pipe											
Sum:	Vo	631,424.28 gal		Vlp1	634,110.75 gal		Vlp2	634,028.08 gal			
		80,822,308 oz.			81,166,175 oz.			81,155,594 oz.			
Vo Restrained	93,312 gal	46,239 gal	100,945 gal	309 gal	16,074 gal	305,508 gal	69,037 gal				
Fwp 1	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237			
Fpp 1	1.002293	1.002656	1.002772	1.001924	1.002143	1.002165	1.002830				
Fpt 1	1.000169	1.000169	1.000169	1.000169	1.000169	1.000169	1.000169	1.000169			
Fwt 1	1.001542	1.001542	1.001542	1.001542	1.001542	1.001542	1.001542	1.001542			
Fpwt 1 = Fpt/Fwt	0.998630	0.998630	0.998630	0.998630	0.998630	0.998630	0.998630	0.998630			
Vlp 1 = Vo(Fwp)(Fpp)(Fpwt)	93,700 gal	46,448 gal	101,413 gal	310 gal	16,139 gal	306,739 gal	69,361 gal				
Fwp 2	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237	1.003237			
Fpp 2	1.002296	1.002659	1.002775	1.001928	1.002147	1.002168	1.002834				
Fpt 2	1.000182	1.000182	1.000182	1.000182	1.000182	1.000182	1.000182	1.000182			
Fwt 2	1.001688	1.001688	1.001688	1.001688	1.001688	1.001688	1.001688	1.001688			
Fpwt 2 = Fpt/Fwt	0.998496	0.998496	0.998496	0.998496	0.998496	0.998496	0.998496	0.998496			
Vlp = Vo(Fwp)(Fpp)(Fpwt)	93,688 gal	46,442 gal	101,400 gal	310 gal	16,137 gal	306,699 gal	69,352 gal				
Combined Pipe											
Sum:	Vo	636,707.27 gal		Vlp1	639,418.89 gal		Vlp2	639,335.66 gal			
		81,498,530 oz.			81,845,618 oz.			81,834,965 oz.			
1 °F Change	83.23 gal	10,653.55 oz.									



## Hydrostatic Test Pipe Data Table

Pipe Type	Length	Restrained / Unrestrained	Outside Diameter	Wall Thickness	Specification & Grade	Pipe Yield Pressure	Material	Joint Type	Seam Type
1	60 ft	Unrestrained	34.000 in.	0.5050 in.	API5L-X60	1,782 psig	Steel	Arc Weld	DSAW
2	1,867 ft	Restrained	36.000 in.	0.5000 in.	API5L-X60	1,667 psig	Steel	Arc Weld	DSAW
3	918 ft	Restrained	36.000 in.	0.4320 in.	API5L-X60	1,440 psig	Steel	Arc Weld	DSAW
4	2,000 ft	Restrained	36.000 in.	0.4140 in.	API5L-X65	1,495 psig	Steel	Arc Weld	DSAW
5	7 ft	Restrained	34.000 in.	0.5620 in.	API5L-X60	1,984 psig	Steel	Arc Weld	DSAW
6	362 ft	Restrained	34.000 in.	0.5050 in.	API5L-X60	1,782 psig	Steel	Arc Weld	DSAW
7	6,876 ft	Restrained	34.000 in.	0.5000 in.	API5L-X46	1,353 psig	Steel	Arc Weld	DSAW
8	1,532 ft	Restrained	34.000 in.	0.3830 in.	API5L-X60	1,352 psig	Steel	Arc Weld	DSAW
9	40 ft	Unrestrained	34.000 in.	0.5000 in.	API5L-X65	1,912 psig	Steel	Arc Weld	DSAW
10	22 ft	Unrestrained	30.000 in.	0.3750 in.	API5L-X60	1,500 psig	Steel	Arc Weld	DSAW
11	3 ft	Unrestrained	24.000 in.	0.3750 in.	API5L-X52	1,625 psig	Steel	Arc Weld	DSAW
12	49 ft	Unrestrained	6.625 in.	0.2800 in.	API5L-Grade B	2,958 psig	Steel	Arc Weld	SM


### Hydrostatic Test Project Owner & Participants

Owner Company	Pacific Gas and Electric Company	Job Number
Address	350 N. Wiget	
	Walnut Creek, CA 94598	41497309
	Attention: Redacted	
Construction Company	Snelson	Job Number
Address	601 West State Street	
	Sedro-Woolley, WA 98284	41474005-T74
	Attention: Redacted	
Hydrostatic Test Co.	Milbar Hydro-test Incorporated	Project No.
Address	P.O. Box 7701	
	Shreveport, Louisiana 71137-7701	FY12-112
Test Section	PG&E T-74 Line 300A, MP 499.77 - 502.23	
	From: 0+00	
	To: 184+08	
File Name	RCP 61362 - T-74, L-300A	


Part II – Test Data (TO BE PREPARED BY PERSON SUPERVISING TEST AT TIME OF TEST)				Note: Minimum test pressure and duration are not to be charged without written approval.			
Time and Date Test Pressure Reached	8/4/11 3:02 AM	Elevation at Test Point	55 ft	Min. Required Test Press At Test Point (1)	1,014.00 psig	Max. Allowable Test Press at Test Point (4)	1,089.83 psig
Time and Date Test Ended	8/4/11 11:45 AM	Max. Elevation in Test Section	55 ft	Min. Indicated Test Pressure (2)	1,023.00 psig	Max. Indicated Test Pressure (5)	1,090.00 psig
Actual Duration of Test	8 hours 43 minutes	Min. Elevation in Test Section	20 ft	Min. Test Pressure at Max. Elevation (3)	1,023.00 psig	Max. Test Pressure at Min. Elevation (6)	1,105.17 psig

RCP

## PG&E T-74 Line 300A, MP 499.77 - 502.23

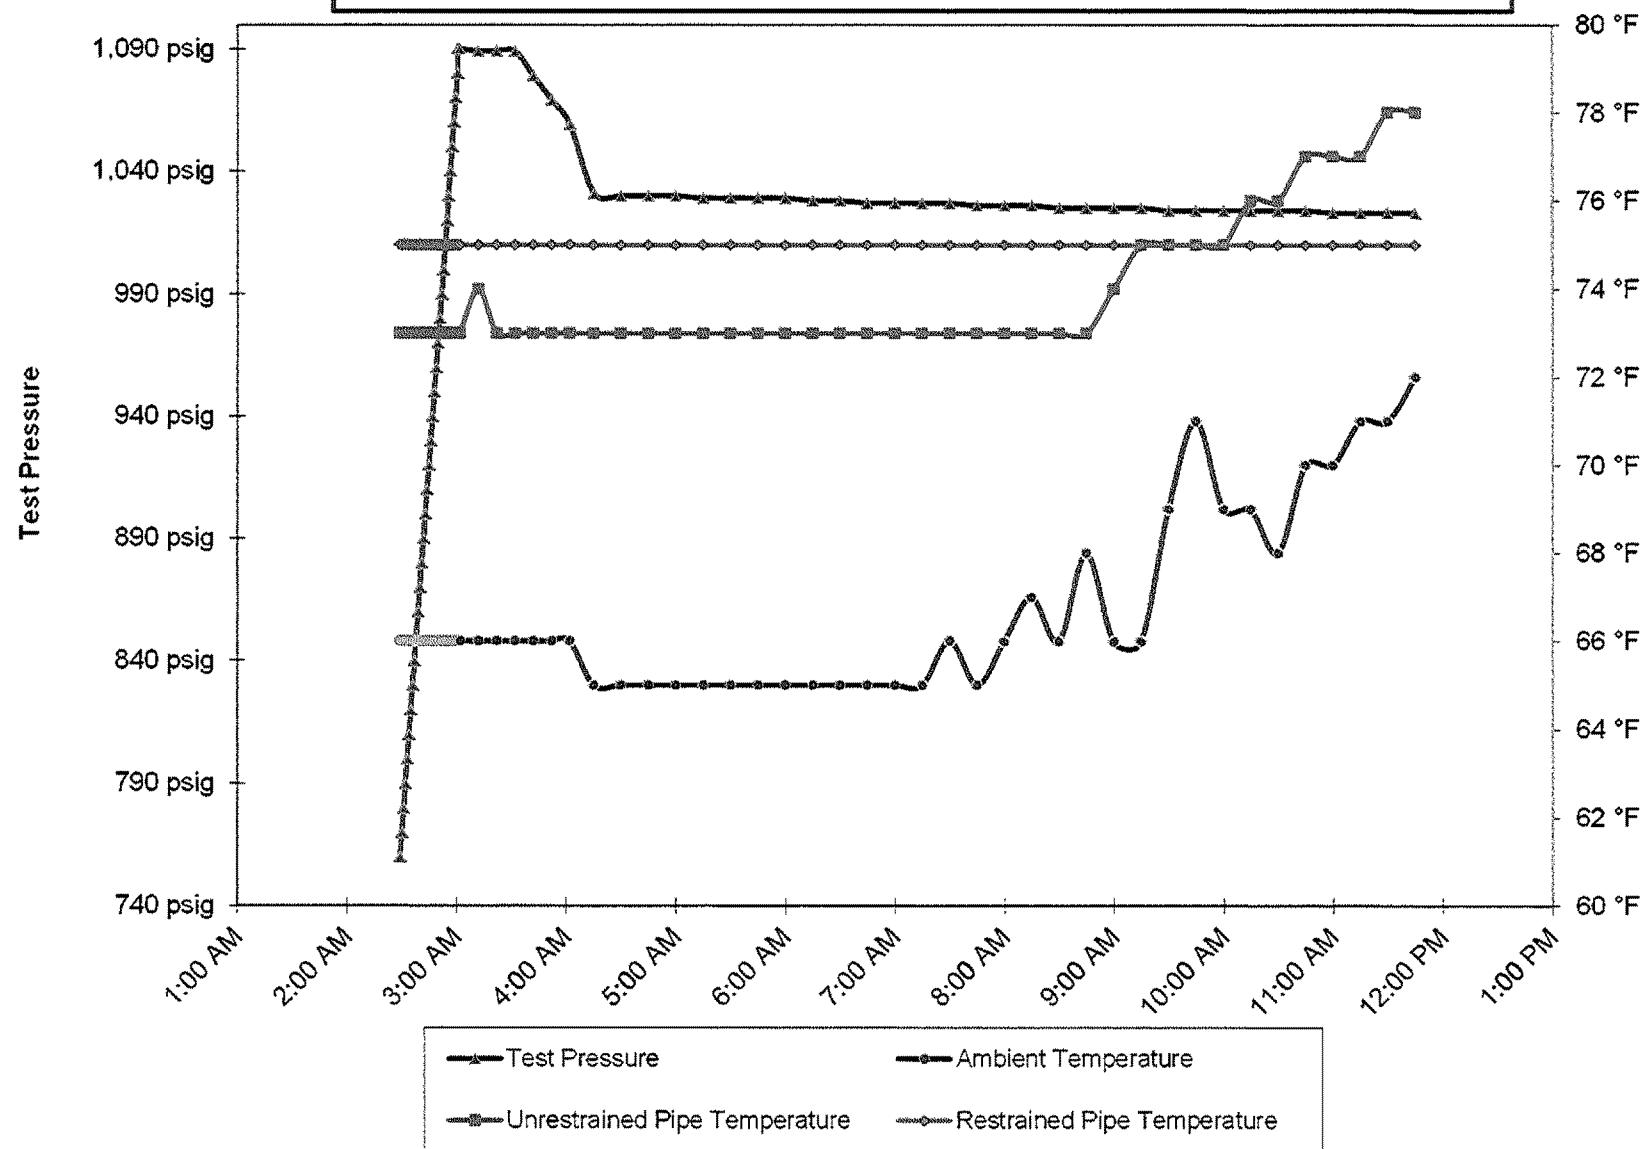

**Spike Pressure Test**  
**Stress Strain Curve -- PG&E T-74 Line 300A, MP 499.77 - 502.23**

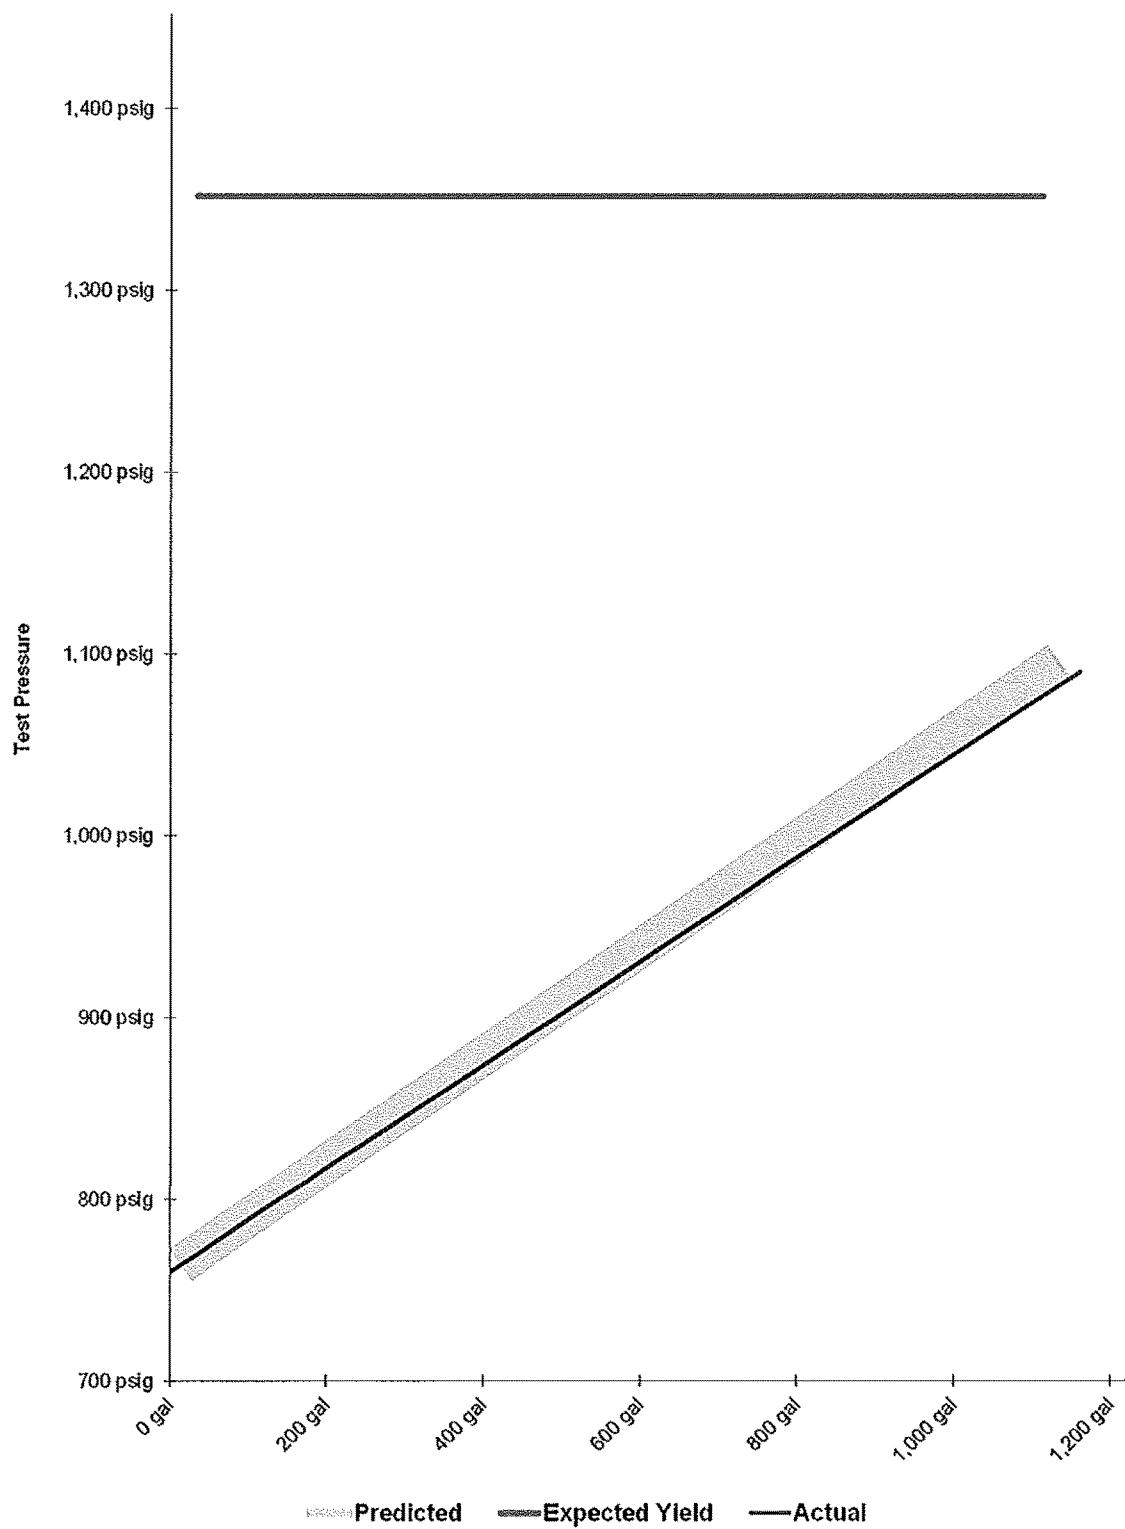

**Redacted**


8/04/11 Date




Test Pump and Trailer




Deadweight tester

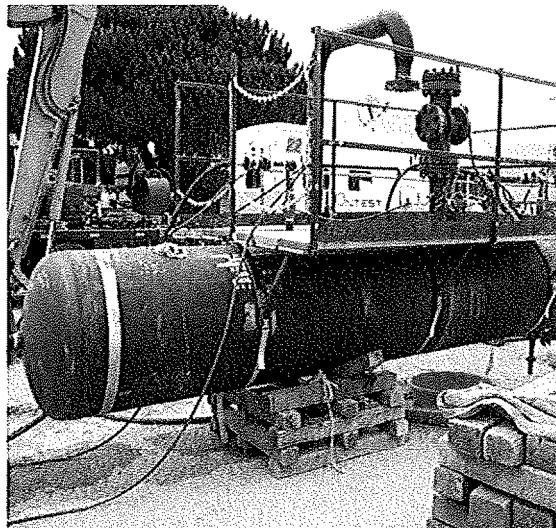

Test Head B

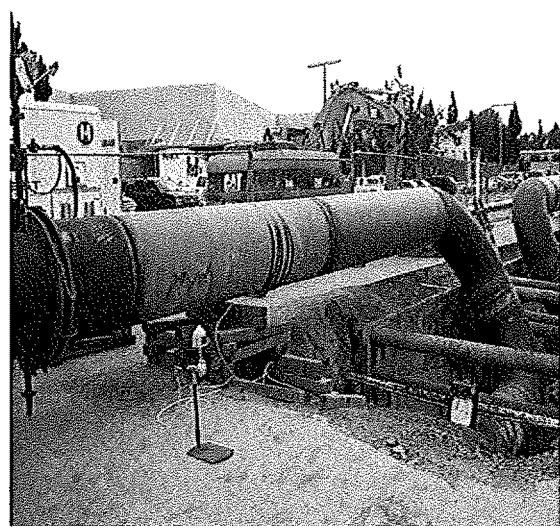

Unrestrained temp Chart

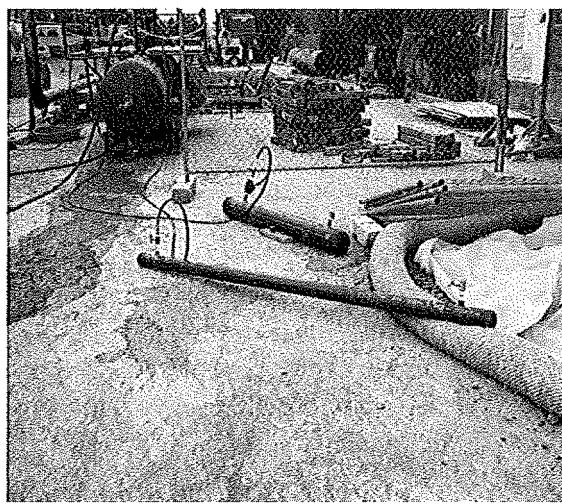

3.5" and 6" part of test



30" Tie-in pipe in test
