



RCP, Inc

801 Louisiana, Ste.200
Houston, Texas 77002

Redacted

October 24, 2011

Pacific Gas and Electric Company
350 N. Wiget
Walnut Creek, CA 94598
Attention Redacted

Test Contractor: ARB - 0629-53-3500 T-43B
Asset Owner: Pacific Gas and Electric Company -- 41497361
Construction Contractor: ARB - 0629-53-3500 T-43B
Test Section: PG&E T-43B , L-147, MP 1.95 - 3.4
Test Date: October 23, 2011
Certificate Number: RCP 61362 - T-43B , L-147, MP 1.95 - 3.4

To whom it may concern,

This letter is to certify that the hydrostatic test performed on pipe owned by Pacific Gas and Electric Company and tested by ARB met the requirements of the Code of Federal Regulations, Title 49, Part 192, Subpart J (Class 3).

The test segment was subjected to a spike pressure test of 748 psig for 30 minutes, without observed leakage or yielding of the pipe segment. The 30 minute spike test and subsequent pressure reduction with volume bleed was included and is part of the 8.32 hour test duration period.

This hydrostatic test was completed successfully. Pressure was maintained on the test facilities in excess of 8.32 continuous hours without evidence of a leak failure. Water was the test medium. At the highest elevation point in the test section, the calculated test pressure was 609 psig and the MAOP per 49 CFR Part 192, Subpart J can be as high as 406 psig. The MAOP established by this test is sufficient to qualify for Pacific Gas and Electric Company's desired MAOP of 400 psig.

Pressure decreased 61 psi during the test. 9,523.20 ounces of fluid was intentionally released from the test section. Net corrected volumetric change from beginning of the test to the end of the test is calculated to be 1,792.68 ounces, gain, which is equivalent to a 1.38 °F change in pipe temperature and larger than the anticipated error attributed to the temperature measurement instrumentation utilized.

Test pressure did not remain steady even though no leaks were observed. The volumetric gain is attributed to the inherent error associated with physically attempting to measure the average temperature of 7,541 feet of buried and 175 feet of exposed pipe from a single point on the line.

Sincerely,

Redacted

cc. file

E:\

MOD T-43B version 10.14.2011
Letter

RCP

Hydrostatic Test Certification

| | | | |
|------------------|--|-------------|--------------------|
| Company | Pacific Gas and Electric Company | Job Number | 41497361 |
| Construction Co. | ARB | Job Number | 0629-53-3500 T-43B |
| Hydro. Test Co. | ARB | Project No. | 0629-53-3500 T-43B |
| Test Section | PG&E T-43B , L-147, MP 1.95 - 3.4 | | |
| File Name | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | |

Hydrostatic Test Pressure

| | | |
|--|------------|-----------|
| APPLICABLE CODE FOR CERTIFICATION: | Test Date: | 23-Oct-11 |
| Code of Federal Regulations, Title 49, Part 192, Subpart J (Class 3) | | |

This is to certify that the pipeline or pipeline section(s) described below was hydrostatically pressure tested in accordance with the following procedure:

Pipeline: PG&E T-43B , L-147, MP 1.95 - 3.4

From: 135+25

To: 60+34

Pipe Data

| Segment | Length | Diameter | Wall Thickness | Specification | 100% SMYS |
|---------|----------|------------|----------------|------------------------------------|-----------|
| 1 | 101 ft | 20.000 in. | 0.375 in. | API5L-XS5, ERW-LF, Arc Weld, Steel | 2,438 psi |
| 2 | 31 ft | 6.625 in. | 0.280 in. | API5L-Grade B, SM, Arc Weld, Steel | 2,958 psi |
| 3 | 25 ft | 3.500 in. | 0.216 in. | API5L-Grade B, SM, Arc Weld, Steel | 4,320 psi |
| 4 | 23 ft | 1.315 in. | 0.154 in. | API5L-Grade B, SM, Arc Weld, Steel | 8,198 psi |
| 5 | 471 ft | 20.000 in. | 0.313 in. | API5L-X42, DSAW, Arc Weld, Steel | 1,313 psi |
| 6 | 1,439 ft | 20.000 in. | 0.250 in. | API5L-X42, DSAW, Arc Weld, Steel | 1,050 psi |
| 7 | 4,959 ft | 20.000 in. | 0.281 in. | API5L-Grade B, SM, Arc Weld, Steel | 984 psi |
| 8 | 134 ft | 20.000 in. | 0.375 in. | API5L-X52, DSAW, Arc Weld, Steel | 1,950 psi |
| 9 | 501 ft | 24.000 in. | 0.313 in. | API5L-X60, DSAW, Arc Weld, Steel | 1,563 psi |
| 10 | 14 ft | 6.625 in. | 0.280 in. | API5L-Grade B, SM, Arc Weld, Steel | 2,958 psi |
| 11 | 18 ft | 20.000 in. | 0.750 in. | API5L-X42, DSAW, Arc Weld, Steel | 3,150 psi |

Initial Test Conditions

| Pressure at Test Point: | 748 psig | Date/Time: | Pipe Temperature | |
|--------------------------------------|----------|-------------------------|------------------|---------------------|
| | | | Unrestrained: | 80.0 °F |
| Ambient Temperature: | 84.0 °F | Elevation @ Test Point: | 16.0 ft | Restrained: 66.0 °F |
| Pressure @ High Point (Cal/Measure): | 670 psig | Elevation @ High Point: | 196.0 ft | Location: 135+25 |
| Pressure @ Low Point (Cal/Measure): | 748 psig | Elevation @ Low Point: | 16.0 ft | Location: 67+09 |
| | | | | Location: 135+25 |

Final Test Conditions

| Pressure at Test Point: | 687 psig | Date/Time: | Pipe Temperature | |
|--------------------------------------|----------|-------------------------|------------------|---------------------|
| | | | Unrestrained: | 77.0 °F |
| Ambient Temperature: | 63.0 °F | Elevation @ Test Point: | 16.0 ft | Restrained: 68.0 °F |
| Pressure @ High Point (Cal/Measure): | 609 psig | Elevation @ High Point: | 196.0 ft | Location: 135+25 |
| Pressure @ Low Point (Cal/Measure): | 687 psig | Elevation @ Low Point: | 16.0 ft | Location: 67+09 |
| Total Fluid Injected: | | | | Location: 135+25 |

Total Fluid Withdrawn: 9523.20 fluid ounces

Volume gain

| | | | | |
|--|-------------|------|---------|---------------------|
| Net Change in Volume of the Test Section ± (+ Gain, - Loss): | 1,792.68 oz | gain | 0.0115% | 1.381 °F equivalent |
|--|-------------|------|---------|---------------------|

Test Duration: 8.32 hours

| Minimum Test Pressure: Maximum Test Pressure: % SMYS : | Test Point | Max Elevation | Pipe Temperature | |
|--|------------|---------------|------------------|----------|
| | | | 685 psig | 685 psig |
| | | | 748 psig | 748 psig |
| 71.3% | | | 9900.0% | 47.9% |

Test Segment Observed % SMYS :

Minimum

6.6%

Maximum

76.0%

Minimum Test Pressure (Calculated/Measured):

609 psig

Maximum Allowable Operating Pressure:

DOT Part 192

Test Factor= 1.50

406 psig

The MAOP established by this test is sufficient to qualify for Pacific Gas and Electric Company's desired MAOP of 400 psig.

| | | |
|------------------------------|-----|---|
| Were leaks observed? | No | Explain: |
| Acceptable Hydrostatic Test? | Yes | <p>The test segment was subjected to a spike pressure test of 748 psig for 30 minutes, without observed leakage or yielding of the pipe segment. The 30 minute spike test and subsequent pressure reduction with volume bleed was included and is part of the 8.32 hour test duration period.</p> <p>No leaks were observed during the test period. The test section included 7,541 feet of buried and 175 feet of exposed pipe. Pressure lost 61 psi during the test. The buried pipe segment gained 2°F fluid temperature and the exposed pipe segment lost 3°F.</p> <p>9,523.20 ounces of fluid was intentionally released from the test section. Net corrected volumetric change from beginning of the test to the end of the test is calculated to be 1,792.68 ounces, gain, which is equivalent to a 1.38 °F change in pipe temperature and larger than the anticipated error attributed to the temperature measurement instrumentation utilized.</p> <p>Test pressure did not remain steady even though no leaks were observed. The volumetric gain is attributed to the inherent error associated with physically attempting to measure the average temperature of 7,541 feet of buried and 175 feet of exposed pipe from a single point on the line.</p> |
| Remarks | | Lots of air was observed in the line during testing due to trapped pigs. The SS curve did not indicate yielding of the pipe. Water truck ran out of water during ramping pressure to spike at 640 psig at 2:13 pm. Continued pressuring to spike pressure after water truck arrived, from 620 psig at 3:35 pm, due to erroneous readings created by injected air. Depressurization was controlled and done very slowly so as not to disturb pigs and cause rapid or irregular pressure readings. |

Redacted

24-Oct-11

Redacted



Dead Weight Log Sheet

| | | | |
|------------------|--|-------------|--------------------|
| Owner Company | Pacific Gas and Electric Company | Job Number | 41497361 |
| Construction Co. | ARB | Job Number | 0629-53-3500 T-43B |
| Testing Co. | ARB | Project No. | 329-53-3500 T-43 |
| Test Section | PG&E T-43B , L-147, MP 1.95 - 3.4 | | |
| File Name | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | |

| Date | | | 23-Oct-11 | Test Log | | | | | |
|---------|-------------|---------|---------------|----------------|--------------|------------|-------------|--|-----------|
| Log No. | Test Period | | Test Pressure | Temperature °F | | | Remarks | | |
| | Date | Time | | Ambient | Unrestrained | Restrained | | | |
| 1 | 10/23/11 | 2:00 PM | 510 psig | 59 °F | 68 °F | 66 °F | Start Spike | | |
| 2 | 10/23/11 | 2:01 PM | 520 psig | 59 °F | 68 °F | 66 °F | Inject | | 938 oz. |
| 3 | 10/23/11 | 2:02 PM | 530 psig | 86 °F | 77 °F | 66 °F | Inject | | 2,481 oz. |
| 4 | 10/23/11 | 2:03 PM | 540 psig | 86 °F | 77 °F | 66 °F | Inject | | 2,879 oz. |
| 5 | 10/23/11 | 2:04 PM | 550 psig | 86 °F | 77 °F | 66 °F | Inject | | 2,529 oz. |
| 6 | 10/23/11 | 2:05 PM | 560 psig | 86 °F | 77 °F | 66 °F | Inject | | 2,227 oz. |
| 7 | 10/23/11 | 2:06 PM | 570 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,972 oz. |
| 8 | 10/23/11 | 2:07 PM | 580 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,933 oz. |
| 9 | 10/23/11 | 2:08 PM | 590 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,829 oz. |
| 10 | 10/23/11 | 2:09 PM | 600 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,678 oz. |
| 11 | 10/23/11 | 2:10 PM | 610 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,646 oz. |
| 12 | 10/23/11 | 3:35 PM | 620 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,591 oz. |
| 13 | 10/23/11 | 3:36 PM | 630 psig | 86 °F | 77 °F | 66 °F | Inject | | 239 oz. |
| 14 | 10/23/11 | 3:37 PM | 640 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,312 oz. |
| 15 | 10/23/11 | 3:38 PM | 650 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,193 oz. |
| 16 | 10/23/11 | 3:39 PM | 660 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,304 oz. |
| 17 | 10/23/11 | 3:40 PM | 670 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,312 oz. |
| 18 | 10/23/11 | 3:41 PM | 680 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,344 oz. |
| 19 | 10/23/11 | 3:42 PM | 690 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,328 oz. |
| 20 | 10/23/11 | 3:43 PM | 700 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,352 oz. |
| 21 | 10/23/11 | 3:44 PM | 710 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,424 oz. |
| 22 | 10/23/11 | 3:45 PM | 720 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,320 oz. |
| 23 | 10/23/11 | 3:46 PM | 730 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,368 oz. |
| 24 | 10/23/11 | 3:47 PM | 740 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,320 oz. |
| 25 | 10/23/11 | 3:48 PM | 748 psig | 86 °F | 77 °F | 66 °F | Inject | | 1,257 oz. |
| 26 | 10/23/11 | 3:56 PM | 748 psig | 84 °F | 80 °F | 66 °F | On Test | | |
| 27 | 10/23/11 | 4:06 PM | 746 psig | 84 °F | 80 °F | 67 °F | | | |
| 28 | 10/23/11 | 4:16 PM | 746 psig | 83 °F | 80 °F | 67 °F | | | |
| 29 | 10/23/11 | 4:26 PM | 745 psig | 82 °F | 80 °F | 67 °F | End Spike | | |
| 30 | 10/23/11 | 4:27 PM | 735 psig | 82 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 31 | 10/23/11 | 4:46 PM | 725 psig | 82 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 32 | 10/23/11 | 5:05 PM | 715 psig | 82 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 33 | 10/23/11 | 5:23 PM | 705 psig | 82 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 34 | 10/23/11 | 5:41 PM | 695 psig | 82 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 35 | 10/23/11 | 5:59 PM | 685 psig | 76 °F | 80 °F | 67 °F | Bleed | | 1,587 oz. |
| 36 | 10/23/11 | 6:00 PM | 685 psig | 76 °F | 80 °F | 67 °F | | | |
| 37 | 10/23/11 | 6:15 PM | 687 psig | 76 °F | 81 °F | 67 °F | | | |
| 38 | 10/23/11 | 6:30 PM | 687 psig | 75 °F | 81 °F | 67 °F | | | |
| 39 | 10/23/11 | 6:45 PM | 687 psig | 75 °F | 81 °F | 67 °F | | | |
| 40 | 10/23/11 | 7:00 PM | 687 psig | 74 °F | 81 °F | 68 °F | | | |
| 41 | 10/23/11 | 7:15 PM | 687 psig | 73 °F | 81 °F | 68 °F | | | |
| 42 | 10/23/11 | 7:30 PM | 687 psig | 73 °F | 81 °F | 68 °F | | | |
| 43 | 10/23/11 | 7:45 PM | 687 psig | 72 °F | 81 °F | 68 °F | | | |
| 44 | 10/23/11 | 8:00 PM | 687 psig | 71 °F | 81 °F | 68 °F | | | |
| 45 | 10/23/11 | 8:15 PM | 687 psig | 71 °F | 81 °F | 68 °F | | | |
| 46 | 10/23/11 | 8:30 PM | 687 psig | 71 °F | 80 °F | 68 °F | | | |
| 47 | 10/23/11 | 8:45 PM | 687 psig | 71 °F | 80 °F | 68 °F | | | |
| 48 | 10/23/11 | 9:00 PM | 687 psig | 69 °F | 80 °F | 68 °F | | | |

Redacted



Pipe Segment Volume Calculations

| | | | | | | | | |
|-----------------------------|--|---------------|---------------|----------------|-------------|--------------------|----------------|------------|
| Company | Pacific Gas and Electric Company | | | | Job Number | 41497361 | | |
| Construction Co. | ARB | | | | Job Number | 0629-53-3500 T-43B | | |
| Hydro. Test Co. | ARB | | | | Project No. | 0629-53-3500 T-43B | | |
| Test Section | PG&E T-43B , L-147, MP 1.95 - 3.4 | | | | | | | |
| File Name | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | | | | | WATER | |
| General Pipe Data | | | | | | | | |
| Description | Segment | | | | | | | |
| | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| Restrained or Unrestrained? | Unrestrained | Unrestrained | Unrestrained | Restrained | Restrained | Restrained | Restrained | Restrained |
| Outside Diameter | 20.000 in. | 6.625 in. | 3.500 in. | 1.315 in. | 20.000 in. | 20.000 in. | 20.000 in. | 20.000 in. |
| Wall Thickness | 0.375 in. | 0.280 in. | 0.216 in. | 0.154 in. | 0.313 in. | 0.250 in. | 0.281 in. | 0.375 in. |
| Inside Diameter | 19.250 in. | 6.065 in. | 3.068 in. | 1.007 in. | 19.375 in. | 19.500 in. | 19.438 in. | 19.250 in. |
| Spec./Grade | API5L-X65 | API5L-Grade B | API5L-Grade B | API5L-Grade B | API5L-X42 | API5L-X42 | API5L-Grade B | API5L-X52 |
| Length Unrestrained | 101 ft | 31 ft | 25 ft | | | | | |
| Length Restrained | | | | 23 ft | 471 ft | 1,439 ft | 4,959 ft | 134 ft |
| Temperature – On Test | 80 °F | 80 °F | 80.0 °F | 66.0 °F | 66.0 °F | 66.0 °F | 66.0 °F | 66.0 °F |
| Temperature – End of Test | 77 °F | 77 °F | 77.0 °F | 68.0 °F | 68.0 °F | 68.0 °F | 68.0 °F | 68.0 °F |
| Pressure – On Test | 748 psig | 748 psig | 748 psig | 748 psig | 748 psig | 748 psig | 748 psig | 748 psig |
| Pressure – End of Test | 687 psig | 687 psig | 687 psig | 687 psig | 687 psig | 687 psig | 687 psig | 687 psig |
| Unrestrained Pipe | | | | | | | | |
| Vo | 1,834.48 gal | | Vtp1 | 1,837.59 gal | | Vtp2 | 1,837.76 gal | |
| | 234,814 oz. | | | 235,212 oz. | | | 235,233 oz. | |
| Vo Unrestrained | 1,527 gal | 47 gal | 10 gal | | | | | |
| Fwp 1 | 1.002290 | 1.002290 | 1.002290 | | | | | |
| Fpp 1 | 1.001600 | 1.000675 | 1.000443 | | | | | |
| Fpt 1 | 1.000364 | 1.000364 | 1.000364 | | | | | |
| Fwt 1 | 1.002418 | 1.002418 | 1.002418 | | | | | |
| Fpwt 1 = Fpt/Fwt | 0.997951 | 0.997951 | 0.997951 | | | | | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | 1,529.82 gal | 46.57 gal | 9.61 gal | | | | | |
| Fwp 2 | 1.002103 | 1.002103 | 1.002103 | | | | | |
| Fpp 2 | 1.001469 | 1.000620 | 1.000407 | | | | | |
| Fpt 2 | 1.000309 | 1.000309 | 1.000309 | | | | | |
| Fwt 2 | 1.001966 | 1.001966 | 1.001966 | | | | | |
| Fpwt 2 = Fpt/Fwt | 0.998347 | 0.998347 | 0.998347 | | | | | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | 1,529.94 gal | 46.57 gal | 9.61 gal | | | | | |
| Restrained Pipe | | | | | | | | |
| Vo | 119,201.49 gal | | Vtp1 | 119,607.53 gal | | Vtp2 | 119,546.97 gal | |
| | 15,257,791 oz. | | | 15,309,764 oz. | | | 15,302,012 oz. | |
| Vo Unrestrained | | | 1 gal | 7.214 gal | 22,325 gal | 78,446 gal | 2,026 gal | |
| Fwp 1 | | | 1.002290 | 1.002290 | 1.002290 | 1.002290 | 1.002290 | 1.002290 |
| Fpp 1 | | | 1.000170 | 1.001428 | 1.001791 | 1.001591 | 1.001186 | |
| Fpt 1 | | | 1.000073 | 1.000073 | 1.000073 | 1.000073 | 1.000073 | 1.000073 |
| Fwt 1 | | | 1.000582 | 1.000582 | 1.000582 | 1.000582 | 1.000582 | 1.000582 |
| Fpwt 1 = Fpt/Fwt | | | 0.999491 | 0.999491 | 0.999491 | 0.999491 | 0.999491 | 0.999491 |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | | | 1 gal | 7,237 gal | 22,405 gal | 76,704 gal | 2,032 gal | |
| Fwp 2 | | | 1.002103 | 1.002103 | 1.002103 | 1.002103 | 1.002103 | 1.002103 |
| Fpp 2 | | | 1.000165 | 1.001321 | 1.001654 | 1.001470 | 1.001099 | |
| Fpt 2 | | | 1.000097 | 1.000097 | 1.000097 | 1.000097 | 1.000097 | 1.000097 |
| Fwt 2 | | | 1.000803 | 1.000803 | 1.000803 | 1.000803 | 1.000803 | 1.000803 |
| Fpwt 2 = Fpt/Fwt | | | 0.999294 | 0.999294 | 0.999294 | 0.999294 | 0.999294 | 0.999294 |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | | | 1 gal | 7,233 gal | 22,393 gal | 76,666 gal | 2,031 gal | |
| Combined Pipe | | | | | | | | |
| Vo | 121,035.98 gal | | Vtp1 | 121,445.12 gal | | Vtp2 | 121,384.73 gal | |
| | 15,492,605 oz. | | | 15,544,976 oz. | | | 15,537,245 oz. | |

RCP

Pipe Segment Volume Calculations

| Company | Pacific Gas and Electric Company | | | | | |
|-----------------------------|--|---------------|--------------|--|--|--|
| Construction Co. | ARB | | | | | |
| Hydro. Test Co. | ARB | | | | | |
| Test Section | PG&E T-43B , L-147, MP 1.95 - 3.4 | | | | | |
| File Name | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | | | | |
| General Pipe Data | | | | | | |
| Description | 9 | 10 | 11 | | | |
| Restrained or Unrestrained? | Restrained | Restrained | Unrestrained | | | |
| Outside Diameter | 24.000 in. | 6.625 in. | 20.000 in. | | | |
| Wall Thickness | 0.313 in. | 0.280 in. | 0.750 in. | | | |
| Inside Diameter | 23.375 in. | 6.065 in. | 18.500 in. | | | |
| Spec./Grade | API5L-X60 | API5L-Grade B | API5L-X42 | | | |
| Length Unrestrained | | | 18 ft | | | |
| Length Restrained | 501 ft | 14 ft | | | | |
| Temperature – On Test | 68.0 °F | 66.0 °F | 80.0 °F | | | |
| Temperature – End of Test | 68.0 °F | 68.0 °F | 77.0 °F | | | |
| Pressure – On Test | 748 psig | 748 psig | 748 psig | | | |
| Pressure – End of Test | 687 psig | 687 psig | 687 psig | | | |
| Unrestrained Pipe | | | | | | |
| Vo | | | | | | |
| Vo Unrestrained | | | 251 gal | | | |
| Fwp 1 | | | 1.002290 | | | |
| Fpp 1 | | | 1.000769 | | | |
| Fpt 1 | | | 1.000364 | | | |
| Fwt 1 | | | 1.002418 | | | |
| Fpwt 1 = Fpt/Fwt | | | 0.997951 | | | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | | | 251.60 gal | | | |
| Fwp 2 | | | 1.002103 | | | |
| Fpp 2 | | | 1.000706 | | | |
| Fpt 2 | | | 1.000309 | | | |
| Fwt 2 | | | 1.001966 | | | |
| Fpwt 2 = Fpt/Fwt | | | 0.998347 | | | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | | | 251.64 gal | | | |
| Restrained Pipe | | | | | | |
| Vo | | | | | | |
| Vo Unrestrained | 11,169 gal | 21 gal | | | | |
| Fwp 1 | 1.002290 | 1.002290 | | | | |
| Fpp 1 | 1.001719 | 1.000513 | | | | |
| Fpt 1 | 1.000073 | 1.000073 | | | | |
| Fwt 1 | 1.000582 | 1.000582 | | | | |
| Fpwt 1 = Fpt/Fwt | 0.999491 | 0.998491 | | | | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | 11,208 gal | 21 gal | | | | |
| Fwp 2 | 1.002103 | 1.002103 | | | | |
| Fpp 2 | 1.001588 | 1.000480 | | | | |
| Fpt 2 | 1.000097 | 1.000097 | | | | |
| Fwt 2 | 1.000803 | 1.000803 | | | | |
| Fpwt 2 = Fpt/Fwt | 0.999294 | 0.999294 | | | | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | 11,202 gal | 21 gal | | | | |
| Combined Pipe | | | | | | |
| Vo | | | | | | |



Pipe Segment Volume Allowance Calculations

| | | | | |
|---|--|---------------|--------------------|----------------|
| Company Construction Co. Hydro. Test Co. Test Section File Name | Pacific Gas and Electric Company | Job Number | 41497361 | WATER |
| | ARB | Job Number | 0629-53-3500 T-43B | |
| | ARB | Project No. | 0629-53-3500 T-43B | |
| | PG&E T-43B , L-147, MP 1.95 - 3.4 | | | |
| | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | | |
| | | | | |
| General Pipe Data | | | | |
| Description | | Segment | | |
| | | 1 | 2 | 3 |
| Restrained or Unrestrained? | Unrestrained | Unrestrained | Unrestrained | Restrained |
| Outside Diameter | 20.000 in. | 6.625 in. | 3.500 in. | 1.315 in. |
| Wall Thickness | 0.375 in. | 0.280 in. | 0.216 in. | 0.154 in. |
| Inside Diameter | 19.250 in. | 6.065 in. | 3.068 in. | 1.007 in. |
| Spec./Grade | API5L-X65 | API5L-Grade B | API5L-Grade B | API5L-Grade B |
| Length Unstrained | 101 ft | 31 ft | 25 ft | |
| Length Restrained | | | | 23 ft |
| Temperature -- On Test | 78 °F | 78 °F | 78 °F | 66 °F |
| Temperature -- End of Test | 79 °F | 79 °F | 79 °F | 67 °F |
| Pressure -- On Test | 717 psig | 717 psig | 717 psig | 717 psig |
| Pressure -- End of Test | 717 psig | 717 psig | 717 psig | 717 psig |
| Unrestrained Pipe | | | | |
| Vo | 1,834.48 gal | Vtp1 | 1,837.78 gal | 1,837.57 gal |
| | 234,814 oz | | 235,236 oz | 235,209 oz |
| Vo Unrestrained | 1,527 gal | 47 gal | 10 gal | |
| Fwp 1 | 1.002195 | 1.002195 | 1.002195 | |
| Fpp 1 | 1.001534 | 1.000647 | 1.000424 | |
| Fpt 1 | 1.000328 | 1.000328 | 1.000328 | |
| Fwt 1 | 1.002122 | 1.002122 | 1.002122 | |
| Fpwt 1 = Fpt/Fwt | 0.998209 | 0.998209 | 0.998209 | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | 1,529.96 gal | 46.57 gal | 9.61 gal | |
| Fwp 2 | 1.002195 | 1.002195 | 1.002195 | |
| Fpp 2 | 1.001534 | 1.000647 | 1.000424 | |
| Fpt 2 | 1.000346 | 1.000346 | 1.000346 | |
| Fwt 2 | 1.002255 | 1.002255 | 1.002255 | |
| Fpwt 2 = Fpt/Fwt | 0.998095 | 0.998095 | 0.998095 | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | 1,529.79 gal | 46.57 gal | 9.61 gal | |
| Restrained Pipe | | | | |
| Vo | 119,201.49 gal | Vtp1 | 119,588.25 gal | 119,578.32 gal |
| | 15,257,791 oz | | 15,307,297 oz | 15,306,025 oz |
| Vo Restrained | | | 1 gal | 7,214 gal |
| Fwp 1 | | | 1.002195 | 1.002195 |
| Fpp 1 | | | 1.000164 | 1.001370 |
| Fpt 1 | | | 1.000073 | 1.000073 |
| Fwt 1 | | | 1.000582 | 1.000582 |
| Fpwt 1 = Fpt/Fwt | | | 0.999491 | 0.999491 |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | | | 1 gal | 7,236 gal |
| Fwp 2 | | | 1.002195 | 1.002195 |
| Fpp 2 | | | 1.000167 | 1.001374 |
| Fpt 2 | | | 1.000085 | 1.000085 |
| Fwt 2 | | | 1.000681 | 1.000681 |
| Fpwt 2 = Fpt/Fwt | | | 0.999404 | 0.999404 |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | | | 1 gal | 7,235 gal |
| Combined Pipe | | | | |
| Vo | 121,035.98 gal | Vtp1 | 121,426.03 gal | 121,415.89 gal |
| | 15,492,605 oz | | 15,542,532 oz | 15,541,234 oz |
| 1 °F Change | 10.14 gal | | 1,298.07 oz | |

E:\

MOD T-43B version 10.14.2011

Allowance



Pipe Segment Volume Allowance Calculations

| | | | | | | |
|-----------------------------|--|---------------|--------------|--|--|--|
| Company Construction Co. | Pacific Gas and Electric Company | | | | | |
| Hydro. Test Co. | ARB | | | | | |
| Test Section | PG&E T-43B, L-147, MP 1.95 - 3.4 | | | | | |
| File Name | RCP 51362 - T-43B , L-147, MP 1.95 - 3.4 | | | | | |
| General Pipe Data | | | | | | |
| Description | 9 | 10 | 11 | | | |
| Restrained or Unrestrained? | Restrained | Restrained | Unrestrained | | | |
| Outside Diameter | 24.000 in. | 6.625 in. | 20.000 in. | | | |
| Wall Thickness | 0.313 in. | 0.280 in. | 0.750 in. | | | |
| Inside Diameter | 23.375 in. | 6.065 in. | 18.500 in. | | | |
| Spec./Grade | API5L-X60 | API5L-Grade B | API5L-X42 | | | |
| Length Unstrained | | | 18 ft | | | |
| Length Restrained | 501 ft | 14 ft | | | | |
| Temperature – On Test | 66 °F | 66 °F | 78 °F | | | |
| Temperature – End of Test | 67 °F | 67 °F | 79 °F | | | |
| Pressure – On Test | 717 psig | 717 psig | 717 psig | | | |
| Pressure – End of Test | 717 psig | 717 psig | 717 psig | | | |
| Unrestrained Pipe | | | | | | |
| Vo | | | | | | |
| Vo Unrestrained | | | 251 gal | | | |
| Fwp 1 | | | 1.002195 | | | |
| Fpp 1 | | | 1.000737 | | | |
| Fpt 1 | | | 1.000328 | | | |
| Fwt 1 | | | 1.002122 | | | |
| Fpwt 1 = Fpt/Fwt | | | 0.998209 | | | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | | | 251.63 gal | | | |
| Fwp 2 | | | 1.002195 | | | |
| Fpp 2 | | | 1.000737 | | | |
| Fpt 2 | | | 1.000346 | | | |
| Fwt 2 | | | 1.002255 | | | |
| Fpwt 2 = Fpt/Fwt | | | 0.998095 | | | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | | | 251.60 gal | | | |
| Restrained Pipe | | | | | | |
| Vo | | | | | | |
| Vo Restrained | 11,169 gal | 21 gal | | | | |
| Fwp 1 | 1.002195 | 1.002195 | | | | |
| Fpp 1 | 1.001648 | 1.000493 | | | | |
| Fpt 1 | 1.000073 | 1.000073 | | | | |
| Fwt 1 | 1.000582 | 1.000582 | | | | |
| Fpwt 1 = Fpt/Fwt | 0.999491 | 0.999491 | | | | |
| Vtp 1 = Vo(Fwp)(Fpp)(Fpwt) | 11,206 gal | 21 gal | | | | |
| Fwp 2 | 1.002195 | 1.002195 | | | | |
| Fpp 2 | 1.001652 | 1.000496 | | | | |
| Fpt 2 | 1.000085 | 1.000085 | | | | |
| Fwt 2 | 1.000681 | 1.000681 | | | | |
| Fpwt 2 = Fpt/Fwt | 0.999404 | 0.999404 | | | | |
| Vtp 2 = Vo(Fwp)(Fpp)(Fpwt) | 11,205 gal | 21 gal | | | | |
| Combined Pipe | | | | | | |
| Vo | | | | | | |
| 1 °F Change | | | | | | |



Hydrostatic Test Pipe Data Table

| Pipe Type | Length | Restrained / Unrestrained | Outside Diameter | Wall Thickness | Specification & Grade | Pipe Yield Pressure | Material | Joint Type | Seam Type |
|-----------|----------|---------------------------|------------------|----------------|-----------------------|---------------------|----------|------------|-----------|
| 1 | 101 ft | Unrestrained | 20.000 in. | 0.3750 in. | API5L-X65 | 2,438 psig | Steel | Arc Weld | ERW-LF |
| 2 | 31 ft | Unrestrained | 6.625 in. | 0.2800 in. | API5L-Grade B | 2,958 psig | Steel | Arc Weld | SM |
| 3 | 25 ft | Unrestrained | 3.500 in. | 0.2160 in. | API5L-Grade B | 4,320 psig | Steel | Arc Weld | SM |
| 4 | 23 ft | Restrained | 1.315 in. | 0.1540 in. | API5L-Grade B | 8,198 psig | Steel | Arc Weld | SM |
| 5 | 471 ft | Restrained | 20.000 in. | 0.3125 in. | API5L-X42 | 1,313 psig | Steel | Arc Weld | DSAW |
| 6 | 1,439 ft | Restrained | 20.000 in. | 0.2500 in. | API5L-X42 | 1,050 psig | Steel | Arc Weld | DSAW |
| 7 | 4,959 ft | Restrained | 20.000 in. | 0.2810 in. | API5L-Grade B | 984 psig | Steel | Arc Weld | SM |
| 8 | 134 ft | Restrained | 20.000 in. | 0.3750 in. | API5L-X52 | 1,950 psig | Steel | Arc Weld | DSAW |
| 9 | 501 ft | Restrained | 24.000 in. | 0.3125 in. | API5L-X60 | 1,563 psig | Steel | Arc Weld | DSAW |
| 10 | 14 ft | Restrained | 6.625 in. | 0.2800 in. | API5L-Grade B | 2,958 psig | Steel | Arc Weld | SM |
| 11 | 18 ft | Unrestrained | 20.000 in. | 0.7500 in. | API5L-X42 | 3,150 psig | Steel | Arc Weld | DSAW |

Hydrostatic Test Project Owner & Participants


| | | | | | | | |
|--|--|--|--------|--|-------------|---|-------------|
| Owner Company | Pacific Gas and Electric Company | Job Number | | | | | |
| Address | 350 N. Wiget Walnut Creek, CA 94598 | 41497361 | | | | | |
| | Attention: Redacted | | | | | | |
| Construction Company | ARB | Job Number | | | | | |
| Address | 1875 Loveridge Road Pittsburg, CA 94565 | 0629-53-3500 T-43B | | | | | |
| | Attention: Redacted | | | | | | |
| Hydrostatic Test Co. | ARB | Project No. | | | | | |
| Address | 1875 Loveridge Road Pittsburg, CA 94565 | 0629-53-3500 T-43B | | | | | |
| | Attention: Redacted | | | | | | |
| Test Section | PG&E T-43B , L-147, MP 1.95 - 3.4 From: 135+25 To: 60+34 | | | | | | |
| File Name | RCP 61362 - T-43B , L-147, MP 1.95 - 3.4 | | | | | | |
| Part II – Test Data (TO BE PREPARED BY PERSON SUPERVISING TEST AT TIME OF TEST) | | Note: Minimum test pressure and duration are not to be changed without written approval. | | | | | |
| Time and Date Test Pressure Reached | 10/23/11 3:56 PM | Elevation at Test Point | 16 ft | Min. Required Test Press At Test Point (1) | 678.00 psig | Max. Allowable Test Press at Test Point (4) | 750.00 psig |
| Time and Date Test Ended | 10/24/11 12:15 AM | Max. Elevation in Test Section | 196 ft | Min. Indicated Test Pressure (2) | 685.00 psig | Max. Indicated Test Pressure (5) | 748.00 psig |
| Actual Duration of Test | 8 hours 19 minutes | Min. Elevation in Test Section | 16 ft | Min. Test Pressure at Max. Elevation (3) | 607.00 psig | Max. Test Pressure at Min. Elevation (6) | 748.00 psig |

E:\

MOD T-43B version 10.14.2011


Pipe

PG&E T-43B , L-147, MP 1.95 - 3.4

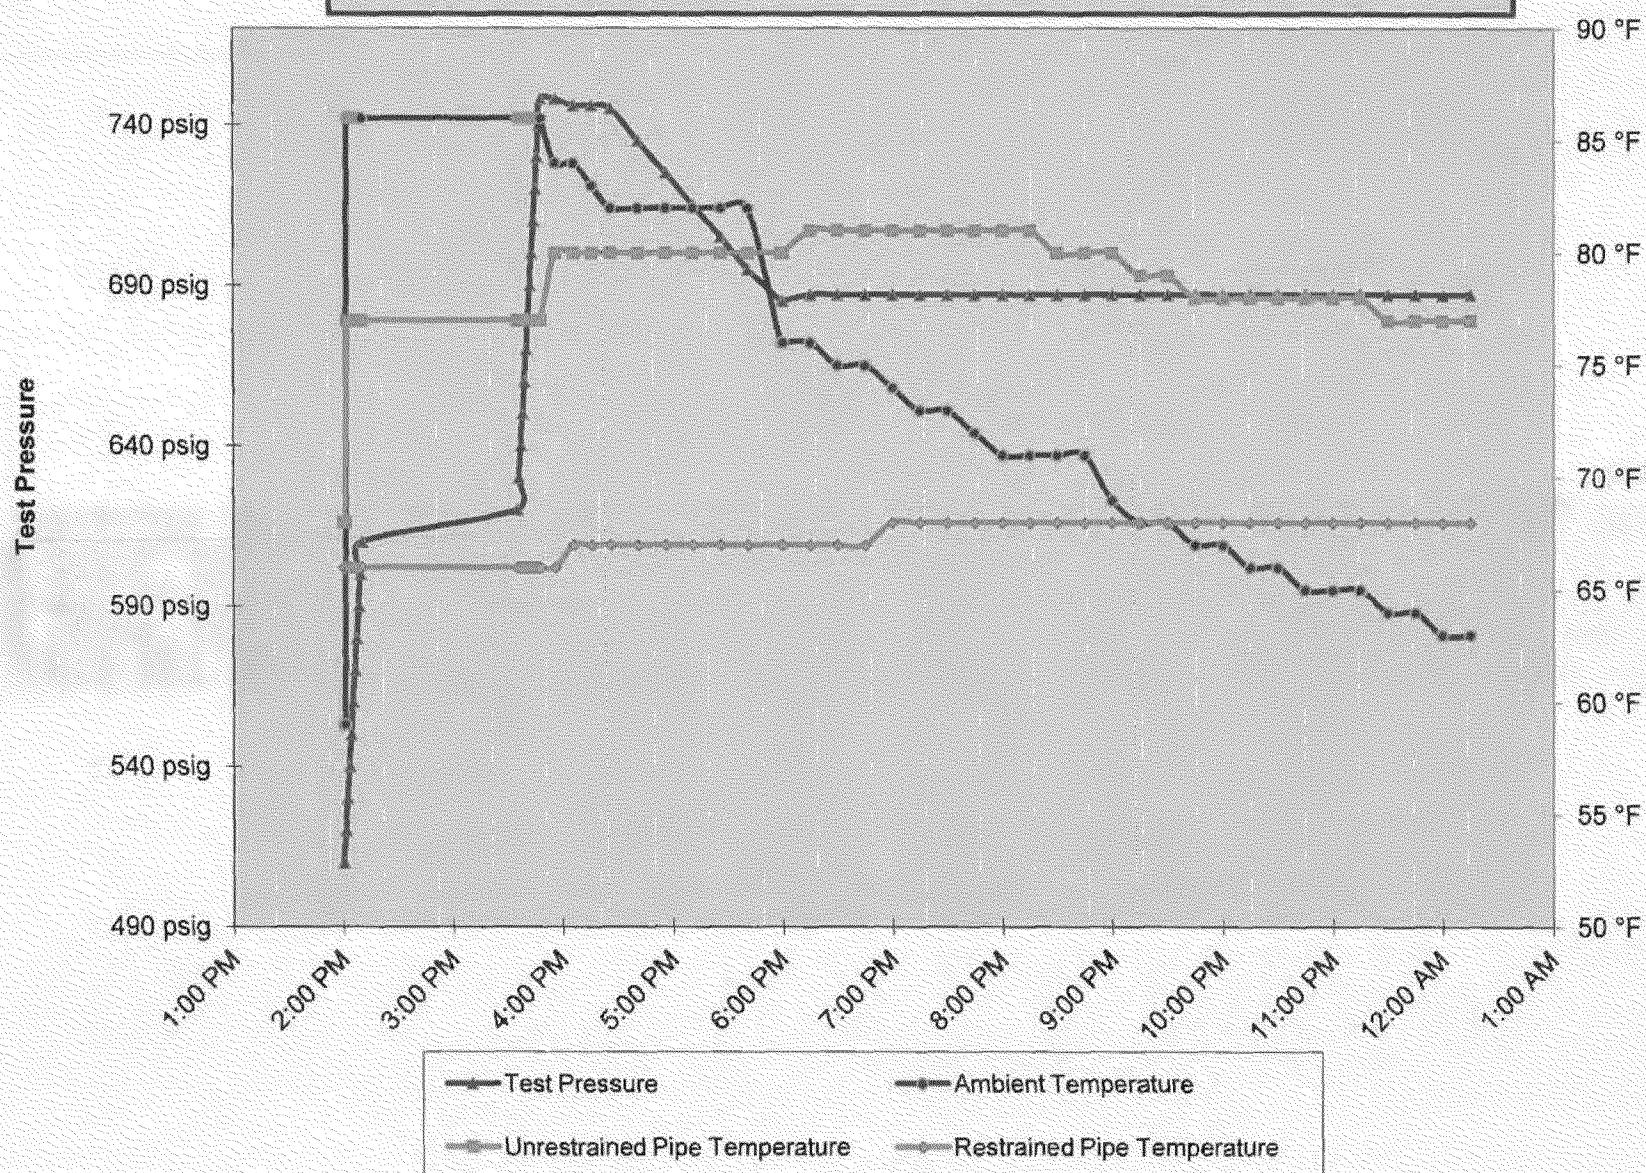


E:\
MOD T-43B version 10.14.2011
PlotT

Spike Pressure Test
Stress Strain Curve -- PG&E T-43B , L-147, MP 1.95 - 3.4

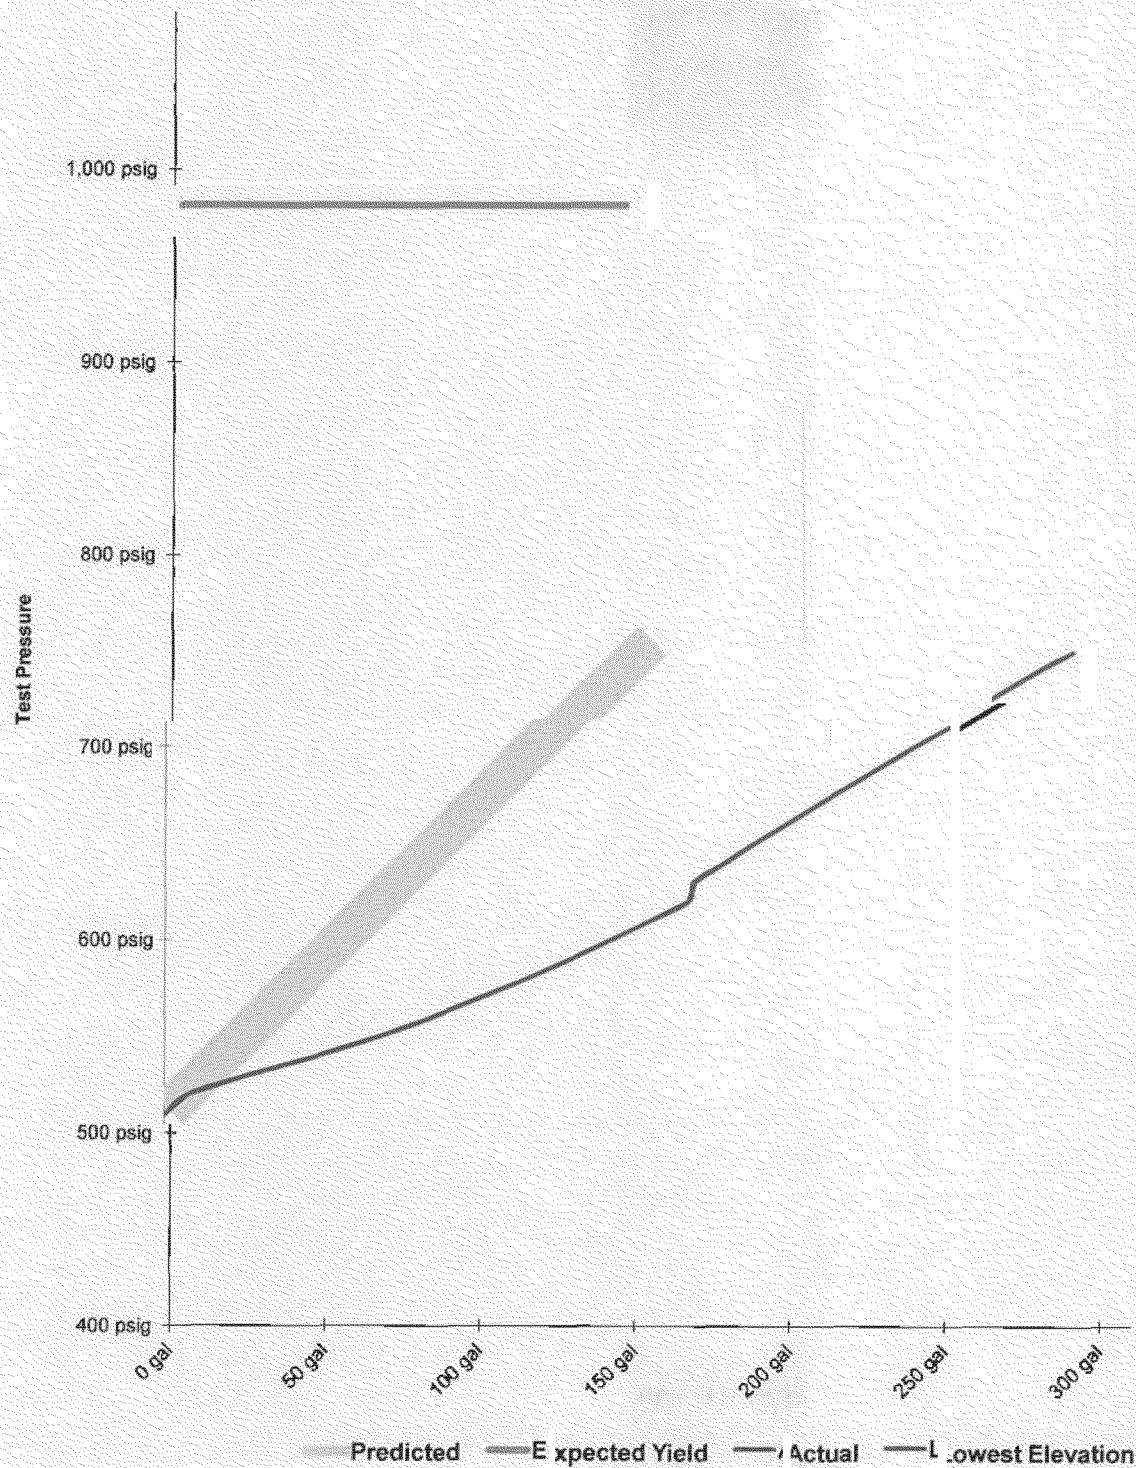




Test End

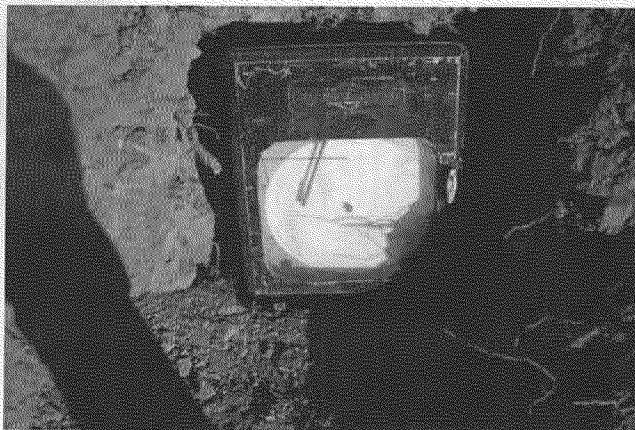

Restrained Temp Recorder Test End



Test Head

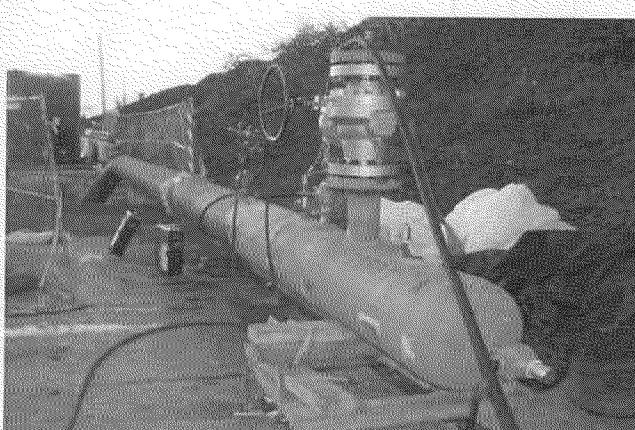


Test Header Connections



Pipe Connect




Unrestrained Temp Recorder

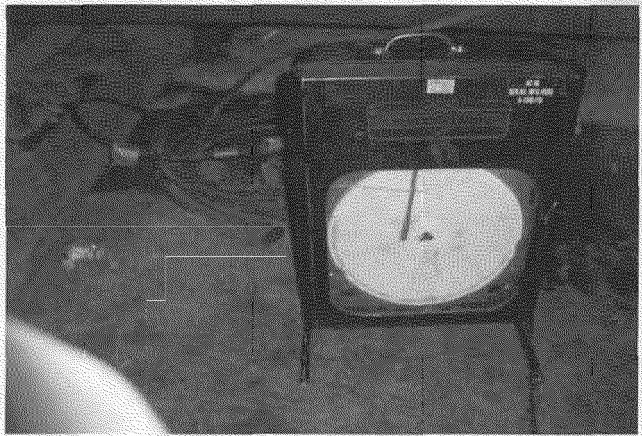


Pressure Chart Recorder



Restrained Pressure Chart Recorder
Test Head

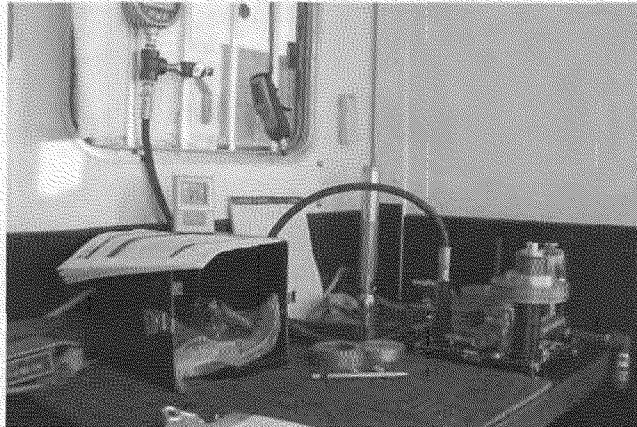

Dead Weight Test Equipment

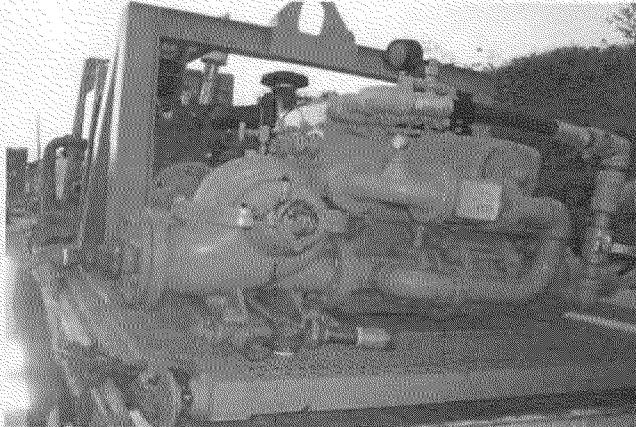

Pressure Pump
