Pacific Gas and Electric Company®

Pipeline Safety Enhancement Program

Master Control Schedule - Milestone by Region/Line

Date	Revision	Checked	Approved
	Data Date: November 15, 2012	JC	PD

Project ID	Line	PSRS ID	PM	City	Var
Bay					41
T-146-12	DFM-0115-C	2633	B Garbe	Oakland	0
T-143-12	DFM-0405-C	2633	S Bombi	Napa	5
T-144-12	DFM-0405-C	2633	S Bombi	Yountville	-14
T-130-12	DFM-3017-C	2632	S Bombi	Walnut Cree	-8
T-131-12	DFM-3017-C	2632	S Bombi	Danville	-8
T-073-12	L-021	2584	S Bombi	San Rafa	0
V-17	L-10	2360	P Chai	Daly Ci	-24
V-19	L-10	2360	P Chai	Daly Ci	-23
V-32	L-10	2428	P Chai	Pittsbur	-34
V-36	L-10	2428	J Mackani	Martine	0
V-37	L-10	2428	P Chai	Hercule	-14
R-18	L-114_	2604	E Star	Oakla	-48
T-172-12	L-13	2546	J Kittle	Livermo	-20
R-17	L-131_	2374	C Ro	Oakla	-67
T-018-12	L-13	2585	S Bombi	San Francisc	-5
T-037-11	L-13	2454	S Bombi	South San Francisc	-9
T-038-11	L-13	2453	S Bombi	San Francisc	0
T-039B-11	L-13	2453	S Bombi	San Francisc	-5
C-019-12	L-15	2585	B Garbe	Oakland	-41
C-020-12	L-15	2585	B Garbe	Oakland	-198
C-047C-11	L-15	2671	B Garbe	Oakland	0
T-019-12	L-15	2647	B Garbe	Oakland	-64
T-020-12	L-15	2647	B Garbe	Oakland	0
T-047C-11	L-15	2647	B Garbe	Oakland	-53
T-179-12	L-153_	2825	B Garbe	Oakland	0
T-021-12	L-191	2585	S Bombi	Pittsbur	0
T-180-12	L-191	2827	M Elmor	Martine	0
R-73	L-210	2752	T Gerbe	Napa	73
T-092-12	L-210	2588	J Kittle	Napa	-18
Ctr Cst					-36
T-024-12	DFM-0813-C	2586	E Zavari	San Jos	-31
T-149-12	DFM-0813-C	2634	E Zavari	San Jos	-31
T-150-12	DFM-0814-C	2634	E Zavari	San Jos	-31
T-096-12	DFM-1816-C	2589	J Arke	Santa Cru	-3
T-101-11	DFM-1816-C	2448	J Arke	Watsonvil	-7
T-025-12	L-10	2586	J Arke	San Jos	-42
T-026-12	L-10	2586	J Arke	San Jos	-42
T-027-12	L-10	2586	J Arke	Milpita	-42
V-22	L-10	2360	J Mackani	Morgan Hi	0
V-23	L-10	2361	J Mackani	San Jos	-27
V-24	L-10	2361	J Mackani	San Jos	0
V-25	L-10	2361	S Kommi	San Jos	0
V-26	L-10	2361	S Kommi	San Jos	0
V-27	L-10	2361	J Mackani	San Jos	0
V-29	L-10	2397	J Mackani	San Juan Bautist	-6
V-09	L-10	2359	J Mackani	Menlo Par	-22
V-11	L-10	2359	J Mackani	San Mate	-37
V-13	L-10	2360	S Kommi	Sunnyva	-26
V-14	L-10	2360	S Kommi	Menlo Par	-40
V-18	L-10	2360	S Kommi	Sunnyva	-13
V-28	L-10	2397	S Kommi	San Mate	-49
R-24	L-10	2600	E Star	Monterey Cn	-12
R-70	L-10	2752	E Star	Monterey Cn	38
T-140-12	L-10	2632	E Zavari	Prunedal	-18
T-142-12	L-10	2632	E Zavari	Salina	-10
T-134A-12	L-10	2631	E Zavari	Sum	24
R-25	L-10	2336	C Richin	Sunnyva	-37
R-26	L-10	2328	C Richin	Santa Clar	0
R-27	L-10	2329	C Richin	Sunnyva	-13
R-28	L-10	2336	C Richin	Santa Clar	78
R-29	L-10	2336	C Richin	Mountain View	-39
T-013A-12	L-10	2583	S Carro	Daly Ci	-101
T-013B-12	L-10	2626	S Carro	Daly Ci	-101
T-114-11	L-10	2517	D Fir	Mountain View	-20
T-123-12	L-10	2632	S Carro	Hillsborou	-46
T-125-12	L-10	2632	E Zavari	Redwood Cit	-2
T-126-12	L-10	2632	E Zavari	Menlo Par	-2
T-175-12	L-10	2813	B Kimbal	Stanfor	-30
T-182-12	L-10	2827	K Takad	Milpita	0
R-21	L-109_2	2572	B Kimbal	Palo Alt	-36
R-22	L-109_2	2572	B Kimbal	Palo Alto/Stanfor	-49
R-30	L-109_3	2601	B Kimbal	Stanford/Menlo Par	-52
R-47	L-109_4	2602	B Kimbal	Santa Clar	-41
R-49	L-109_4	2602	B Kimbal	Santa Clar	-32
T-025B-11	L-13	2774	S Carro	Santa Clar	18
T-104-12	L-13	2591	S Carro	San Carlo	-27
R-20	L-181	2377	C Richin	Monterey Cn	-2
T-159-12	L-181	2631	E Zavari	Aroma	-15
T-110-12	L-300	2592	E Zavari	Hollist	47
T-176-12	L-300	2777	J Arke	Marin	0
V-02		2336	J Mackani	San Mate	0
V-03		2343	J Mackani	San Bruno	0
V-04		2343	J Mackani	San Mate	0
V-07		2344	J Mackani	Milpita	0
Ctr Vly					0
T-136-12	DFM-1616-C	2632	J Kittle	Loc	0
T-168-12	DFM-1616-C	2662	J Kittle	Loc	12
T-173-12	DFM-1728-C	2756	J Arke	Modesto	0
T-040-12	DFM-1721-1	2589	B Kimbal	Modesto	0
T-160-12	DFM-1722-C	2683	J Arke	Turloc	9
T-161-12	DFM-1723-C	2634	B Garbe	Modesto	-16
T-133-12	DFM-1724-C	2631	J Kittle	Modesto	-22
T-162-12	DFM-1724-C	2347	J Kittle	Modesto	-128
R-50	L-108_11	2687	T Gerbe	Loc	-73
R-75	L-109_3	2784	L Cople	Stockto	0
R-76	L-109_3	2370	L Cople	Cere	0
R-06	L-111	2602	K Furlai	Fresn	-39
T-102A-12	L-116	2590	M Elmor	Fresn	13
T-102D-12	L-116	2590	B Kimbal	Chowchil	8
T-102F-12	L-116	2591	J Kittle	Merced	3
R-05	L-13	2603	K Furlai	Fresn	-38
T-044-12	L-13	2589	M Elmor	Fresn	-7
T-045-12	L-13	2590	M Elmor	Fresn	10
T-047-12	L-13	2581	M Elmor	Fresn	6
R-77	L-138	2780	L Cople	Fresn	0
T-155-12	L-138	2631	M Elmor	Fresn	-49
T-048-12	L-142	2581	M Elmor	Bakersfie	-2
T-049-12	L-142	2581	M Elmor	Bakersfie	-3
R-04	L-142	2381	K Furlai	Bakersfie	-12
T-052-12	L-142	2582	M Elmor	Bakersfie	10
T-053-12	L-142	2582	M Elmor	Bakersfie	32
T-054-12	L-142	2582	M Elmor	Bakersfie	42
T-097-12	L-147	2589	B Kimbal	Modesto	0
T-099-12	L-147	2589	B Kimbal	Modesto	1
T-100-12	L-147	2590	B Kimbal	Modesto	-1
R-74	L-167	2775	E Candanoz	Coalinga	-10
T-169-12	L-197	2662	J Kittle	Loc	-17
I-04	L-300	2402	E Candanoz	Fresn	-35
T-055-12	L-300	2582	M Elmor	Tehachap	-1
T-057E-11	L-300	2449	B Garbe	San Bernardin	0

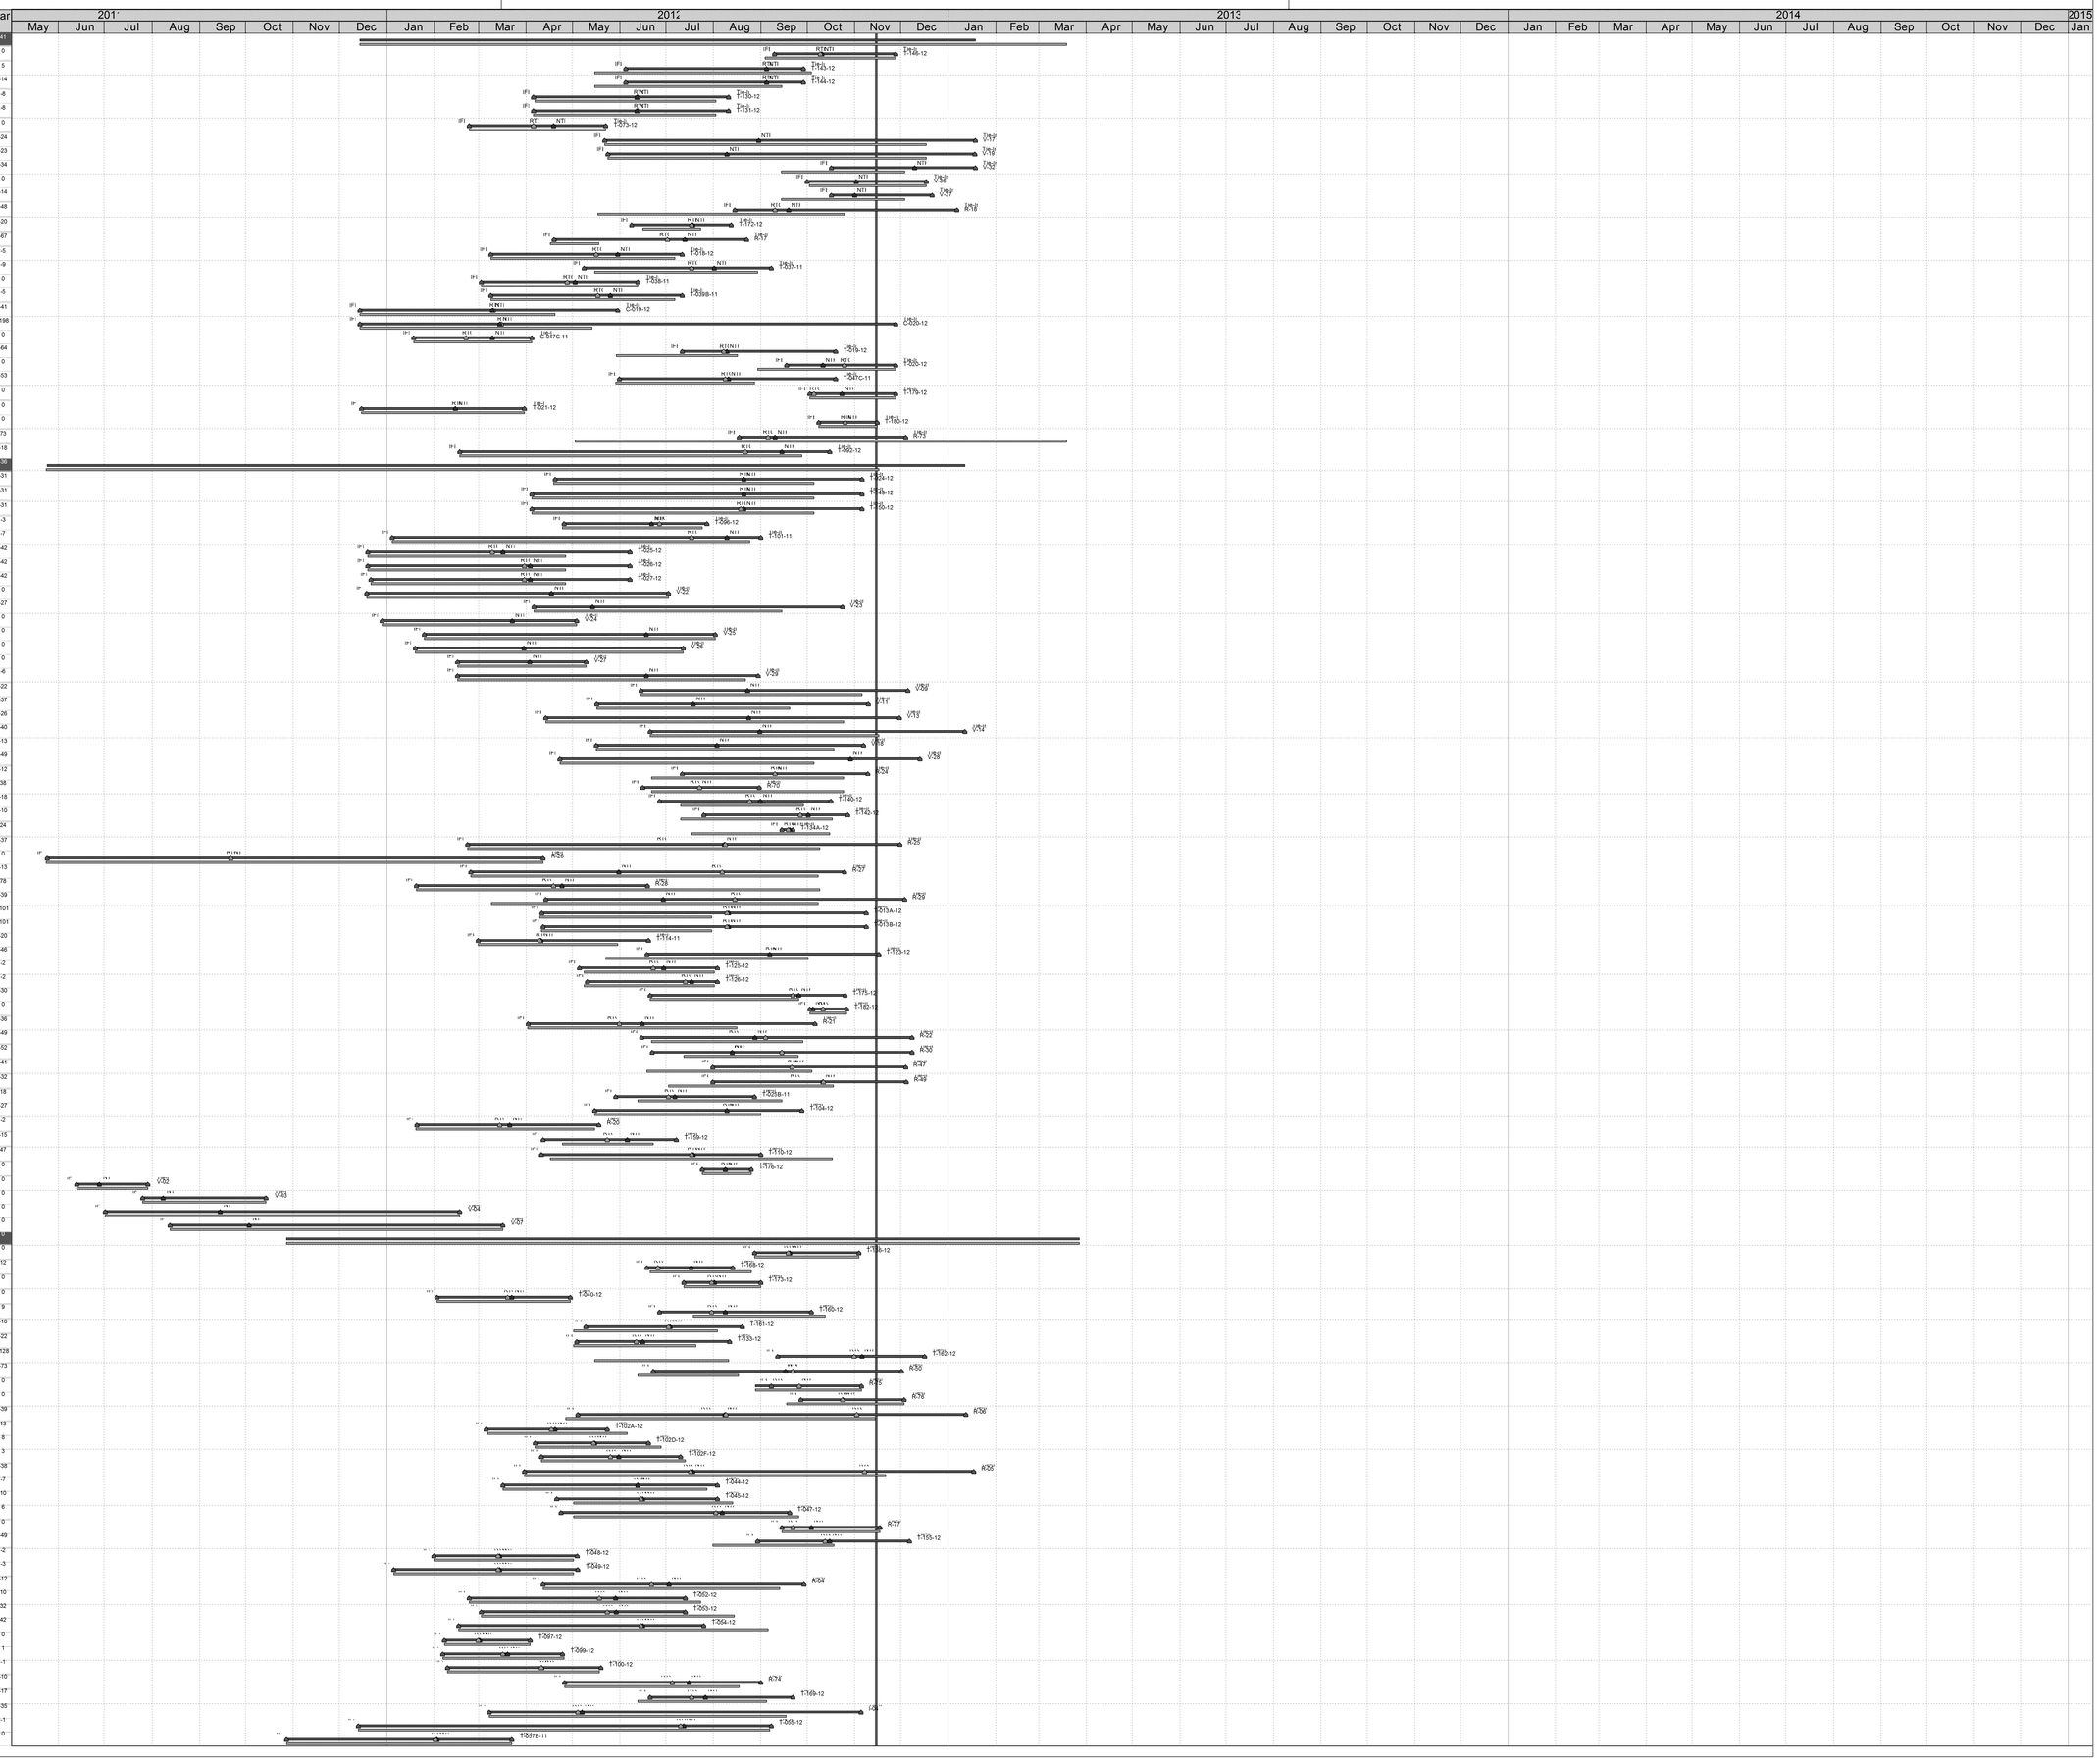

Project ID	Line	PSRS ID	PM	City	Var
T-057W-11	L-300	2678	B Garb	Ker	0
T-059-12	L-300	2583	M Elmo	Bakersfiel	13
T-061-12	L-300	2539	M Elmo	Coaling	0
I-02	L-300	2401	E Candanoz	King	-26
T-122-12	L-300	2592	D Fir	Topoc	0
T-183-12	L-300	2845	J Kittle	Barstov	0
T-183-12	L-300	2845	J Kittle	Barstov	0
T-183-12	L-300	2845	J Kittle	Barstov	0
T-183-12	L-300	2845	J Kittle	Barstov	0
T-183-12	L-300	2845	J Kittle	Barstov	0
R-003		2601	E Candanoz	Modest	0
R-02		1803	E Candanoz	Modest	-41
North					-28
R-41	DFM-1020-C	2380	T Gerbe	Butt	-109
T-166-12	DFM-1301-C	2662	J Kittle	Cota	-22
R-71	DFM-1502-C	2386	T Gerbe	Yuba	-28
R-72	DFM-1503-C	2387	T Gerbe	Yuba	-18
T-079-12	L-119	2585	B Garb	Dav	0
T-177-12	L-119	2813	K Takad	Sacrament	0
R-12	L-16	2379	T Gerbe	Butt	-51
R-13	L-210	2757	T Gerbe	Fairfiel	-20
T-089-12	L-210	2587	B Garb	Fairfiel	-28
T-090-12	L-210	2587	B Garb	Fairfiel	0
T-091-12	L-210	2588	B Garb	Fairfiel	0

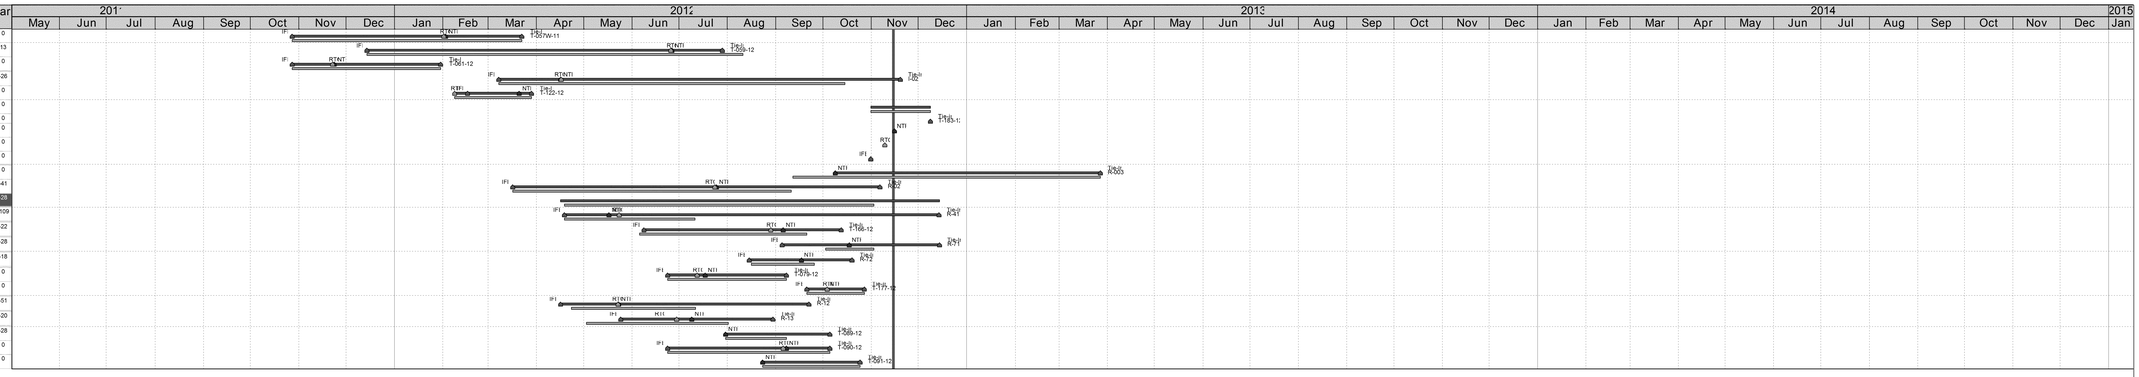

Baseline
IFB
RTC
NTP
Tie in
All Project Phase
Late Finish

Master Schedule
Page 2 of 2
MSC-02

Report Date:28-Nov-12
